



Community Based Approach to Local Development Project



SECOND QUARTERLY PROGRESS REPORT April – June 2009

Executive Summary	4
	5
Statistical Abstract	
I. Context	6
II. Project Activities and Results	9
2.1 Establishing Partnership	10
2.2 Institutionalizing Partnership	12
2.3 Organizing Local Communities	14
2.4 Developing Capacity	21
2.5 Community Plans	24
2.6 Communication and visibility	33
2.7 Advisory and Management	37
III. Lessons And Opportunities	40
IV. Annexure	43 - 80

TABLE OF CONTENTS

Executive Summary	4
Statistical Absrtact	5
I. Context	6
1.1 Project Genesis	7
1.3 Project Area	8
II. Project Activities and Results	9
2.1 Establishing Partnership with Regional/Local Authorities.. ..	10
2.2 Institutionalization of Partnership with Local Authorities.....	12
2.3 Organizing Local Communities	14
2.4 Developing Capacity	21
2.5 Community Development Plans (CDP)	24
2.6 Communication and visibility	33
2.7 Advisory and Management	37
III. Lessons And Opportunities	40
3.1 Lessons Learned	41
3.2 Outlook for Future	42
IV. Annexure	43 - 80

LIST OF ABBREVIATIONS

ARC	Autonomous Republic of Crimea
CBA	Community Based Approach to Local Development Project
CDO	Community Development Officer
CDP	Community Development Plan
CO-MT	Community Organization Management Team
EC	European Commission
EU	European Union
LDF	Local Development Forum
MoU	Memorandum of Understanding
MP	Micro Project
MPP	Micro Project Proposal
OC	Oblast Council
OCC	Oblast Coordination Council
OCRC	Oblast Community Resource Centre (same as OIU)
OIU	Oblast Implementation Unit (same as OCRC)
OSA	Oblast State Administration
PA	Partnership Agreement
PMU	Project Management Unit
RC	Rayon Council
RSA	Rayon State Administration
UNDP	United Nations Development Programme

ACKNOWLEDGEMENT TO OUR PARTNERS

Ministry of Regional
Development and
Construction



Secretariat of the
Cabinet of Ministers of
Ukraine



Cabinet of
Ministers and
Supreme Council
of ARC




Cherkaska Oblast
State
Administration
and Council



Chernihivska
Oblast State
Administration
and Council



Chernivetska
Oblast State
Administration
and Council



Dnipropetrovska
Oblast Council



Ivano-
Frankivska
Oblast State
Administration
and Council



Kharkivska
Oblast State
Administration
and Council



Khersonska
Oblast State
Administration
and Council



Kirovohradska
Oblast State
Administration
and Council



Khmelnytska
Oblast State
Administration
and Council



Kyivska
Oblast State
Administration
and Council



Lvivska
Oblast State
Administration
and Council



Luhanska
Oblast State
Administration
and Council



Mykolaivska
Oblast State
Administration
and Council



Odeska
Oblast State
Administration




Poltavska
Oblast State
Administration
and Council



Rivnenska
Oblast State
Administration
and Council



Sumська
Oblast State
Administration
and Council



Vinnytska
Oblast State
Administration
and Council



Volynska
Oblast State
Administration
and Council



Ternopil'ska
Oblast
Administration
and Council



Zakarpatska
Oblast State
Administration
and Council



Zaporizka Oblast
State
Administration
and Council



Zhytomyrska
Oblast State
Administration

We acknowledge the support and cooperation on the part of the Government of Ukraine (especially the Secretariat of Cabinet of Ministers and the Ministry of Regional Development and Construction) and our regional partners, namely Oblast State Administrations and Oblast Councils. We also acknowledge the support of all pilot rayon authorities (rayon state administrations and councils) and village/city councils that are the partners of CBA Project for their support in CBA implementation.

Similarly, CBA team would like to thank all the institutions/individuals involved in the implementation process for their cooperation during the quarter, namely EC Delegation Office and UNDP management, Crimea Integration and Development Programme, officials of oblast and rayon state administrations/councils, NGOs, media, other public and private agencies.

EXECUTIVE SUMMARY

Community Based Approach to Local Development Project (CBA) was launched in December 2007 with objective to improve living condition of the people across Ukraine through improved service delivery and participatory governance. Following summary of activities and statistical abstract highlight on its achievements during 2nd quarter of 2009:

In the second quarter of 2009, implementation of CBA Project continued, with regional launching completed, and selection of pilot rayons and communities approaching the end. Other important process e.g. institutional development, capacity building, participatory planning, plan mainstreaming, implementation of community initiatives took place albeit at different scale. Details about key activities are given hereunder:

Partnership Agreements were signed with 2 oblasts: Dnipropetrovska and Odeska. Selection of 8 pilot rayons was completed in Donetsk oblast, reaching 100% coverage of the target rayons. In total, 200 rayons and one city council (of oblast subjugation) were selected in all regions. Following to the rayon selection, a net of 34 village/city councils were selected in 15 regions during the quarter. In total, selection of 995 village/city councils was completed by end of 2nd quarter 2009.

In the reported period, focus of Project activities shifted to community mobilization and micro-project proposals. Through community dialogues, 51 new Community Organizations were formed in second quarter with participation of additional 76,709 households. In total, number of COs formed since inception amounts to 961 with involvement of 235,396 persons (59% female). To facilitate the process, CO-manual was published and disseminated.

132 training courses were held during the quarter to build capacity of community activists as well as focal persons from local governments. In cumulatively term, 593 trainings were held for about 14 069 persons (77% CO-members, 23% officials from local authorities).

219 COs prepared community development plans during the quarter. Of them 197 plans were approved by the Local Development Forum. Since inception 871 were prepared by COs. Priority in the plans was focused on energy savings (53%), followed by healthcare services (22%), water supply (19%) and others (6%).

In the reported period, 142 community micro-project proposals were approved by CBA for funding. During the quarter, financing was released (from CBA project side) for new 73 and 10 on-going community projects, amounting to UAH 1.45 mln. Total cost of all the 247 projects approved since inception is UAH 34.9 million of which 8% came from the beneficiary COs, 9% from the village/city councils, 30% from the rayon authorities, 6% from oblast authorities, 1% from the private sectors and remaining 46% from the CBA.

Extensive media coverage of Project activities in the regions was traced. During the quarter, 204 media coverages were registered across Ukraine, including printed and electronic editions, radio and TV reportages. Total coverage since inception amounts to 1209. Also, 36 issues of regional newsletters were published and disseminated among target audience during the quarter besides 82 news posted on various websites.

Six visits were organized at community level during the quarter to familiarize the representatives of government and donors about process and results of CBA implementation. The visitors comprised of representative of Secretariat of the Cabinet of Ministers of Ukraine, Department of Regional Policy; Head of the Delegation of the European Commission to Ukraine and Ambassadors of Great Britain and Sweden; representatives of British, Hungarian, German and Polish embassies; Deputy Director, UNDP Regional Bureau for Europe and the CIS and senior management of UNDP/Ukraine.

In the 3rd quarter of 2009, target will be accomplished in terms of partnership with the regions, rayons, VC/CCs and COs. Focus will be placed on capacity building, planning and implementation of community initiatives. Also, documentation and dissemination of lessons learned will be carried out.

STATISTICAL ABSTRACT

Indicators and Variables	Target	Achievement				
		2008	2009			Cumulative
			Q1	Q2	Sub-total	
PA Signed With Regions	25	22	0	2	2	24
Rayons selected	200	193*	8	0	8	201*
PA Signed With Rayons	200	177	2	9	11	188
VC/CC Selected	1000	961	0	34	34	995
PA Signed With VC/CC	1000	420	125	54	179	599
Communities Selected	1000	876	83	4	87	963
Community Organisation (CO)						
Created	1000	709	201	51	252	961
Registered at VC	1000	550	233	113	346	896
Legally Registered	1000	400	262	133	395	795
Net HH Participation/Membership**						
Target Households (cumulative)	-	267876	240833	267762	267762	267762
Household Participated	-	82 122	36 881	76 709	113 590	195 712
HH Participation Level (cum.)		31%	49%	73%	73%	73%
CO-Members – Total	-	96 698	43 111	95 587	136 698	235 396
CO-Members – Female	-	60.1	68.7	55.0	57.9	59.0
CO-Members – Male	-	39.9	31.3	45.0	42.1	41.0
LDF Created	200	98	48	35	83	181
LDF Sitzings Held	-	107	93	139	232	339
OCC Created	25	6	4	8	12	18
OCC Sitzings Held	-	8	2	11	13	21
Rayon Resource Centers Created	200	10	28	55	83	93
Human Resource Development	-					
No of trainings	-	304	157	132	289	593
No of participants	-	7375	3638	3056	6694	14069
CO-members	-	5584	2917	2309	5226	10810
Local authorities	-	1791	721	747	1468	3259
Community Planning	-					
No. of CO with CDP	1000	389	263	219	482	871
CDP Approved at LDF	1000	232	207	197	404	636
Micro-Project (MP) Proposals						
Approved by LDF	1175	122	127	205	332	454
Submitted to CBA	1175	62	82	190	272	334
Approved by CBA	1175	47	58	142	200	247
Total cost (UAH million)		6.31	8.56	20.02	28.58	34.89
Share of CO (%)		10.2	7.8	7.8	7.8	8.3
Share of VC/CC (%)		14.6	9.1	7.5	8.0	9.2
Share of rayon/oblast (%)		36.2	33.6	36.6	35.8	35.8
Share of CBA (%)		38.5	47.3	47.4	47.3	45.7
Share from others (%)		0.5	2.2	0.7	1.1	1.0
Beneficiary Population	-	39 417	68 335	115 451	183 786	223 203
Number of MPs funded by CBA	1175	12	37	73	110	122
Amount Committed (UAH '000)		2 432.2	4048.2	9 481.7	13 529.9	15 962.10
Amount Released (UAH'000)		211.2	508.4	1 445.5	1 953.9	2 165.1
MPs Completed	1175	-	2	5	7	7
Communication and PR						
Press Conferences	-	31	12	21	33	64
Media Coverage	-	753	252	204	456	1209
Publications at web sites	-	203	85	82	167	370

* Includes a city council of oblast subjugation

** Addition/deletion in the number of communities took place from time to time in the regions. As a result, number of HHs and membership also changed accordingly. The data indicate net of the changes.

CHAPTER I



CONTEXT

- 1.1 Project Genesis
- 1.2 Project Area

1.1 PROJECT GENESIS

1.1.1 Background

Ukraine has made significant economic development since its independence. However, it is still challenged by some serious issues. Economic growth is not equitable, with only small share of population benefiting from its fruit. Those who suffer most live in rural and semi-urban areas. Low living standards in these areas are characterized, besides low income, by insufficient access to medical care and education, underdeveloped (or worn out) basic infrastructure and poor access to drinking water. Social, health and environmental problems at local level have is very common and warrant serious attention.

These challenges form a part of the MDG signed by Ukraine in 2000. To achieve these goals, much work is needed, especially at local level. The experience around the world¹ indicate that solution to these challenges is contingent on empowerment and active involvement of local communities, and their capacity to identify development priorities and ensure their attainment. However, legacy of the highly centralised system of policy, planning, budgeting and decision-making is yet to be adequately geared towards accommodating the needs and priorities as perceived by citizens and local authorities. On the other hand, passive attitude of the population in general and limited capacity of the local governments in rural areas to generate revenue remains a challenge.

Experience of European Commission's projects on pilot models for sustainable regional and local development have indicated the need to emphasize 'bottom-up' approach in tackling social needs of the poor population. On the other hand, Area-Based Development (ABD) Approach promoted by UNDP Ukraine through its projects² has proven to be an effective way of achieving social goals in a decentralised manner. In close partnership with local authorities and local communities, ABD Approach unleashes the potential of the people to help themselves. It brings local authorities and communities together for joint problem-solving and development activities, thus reinforcing the MDGs.

Joint EC-UNDP initiative - the Community-Based Approach to Local Development (CBA) is founded on the achievements of ABD approach and is meant for applying its main tenets country-wide and provide valuable inputs for the ongoing policy debate on administrative and fiscal decentralisation and further democratisation of society. CBA Project commenced in December 2007 and functioning since January 2008.

1.1.2 Objectives

Main objective of the CBA Project is to create enabling environment for long-term self-sustaining social-economic and environmental development at local level throughout Ukraine.

Specific objectives of the Project are to:

- Improve living conditions in rural and (semi-) urban communities through sustainable community-based self-help initiatives;
- Demonstrate participatory local governance, joint decision making and public private partnership for decentralised public service delivery through self-governing community organisations;
- Enhance professional skills and knowledge of community organizations and local authorities to initiate and maintain participatory local process on sustainable social economic development and public services delivery;
- Document experience on participatory planning, decision-making and social action with a view to providing inputs for policy and legal reforms.

1.1.3 Project Strategy

The strategic goal of the CBA is to build capacity for participation of the local communities and local authorities into joint decision making process and use this capacity for multi-stakeholders cooperation and multi-sectoral interventions that are geared towards strengthening of local governance and sustainable

¹ As reflected in the conclusions of the World Summit (1992) at Rio de Janeiro and World Summit (2002) at Johannesburg. Local Agenda 21 (www.un.org/esa/sustdev/agenda21.htm) and Johannesburg Declaration (www.un.org/esa/sustdev/documents/Johannesburg%20Declaration.doc) may be browsed for details.

² Crimea Integration and Development Programme (CIDP); Chernobyl Recovery and Development Programme (CRDP); and Municipal Governance and Sustainable Development Programme (MGSDP)

human development with ensured local ownership of the process. To this end, following strategies are followed to materialise the objectives of the Programme.

All oblasts of Ukraine and in Autonomous Republic of Crimea form the overall project area of CBA while selected rayons, village/city councils and local communities form the functional area. Selection is based on the level of socio-economic hardship facing them. Partnership based on willingness and commitment for cost sharing, form the basis of Project implementation in the selected area.

ABD approach is utilized to unleash the potentials of selected communities to address their common needs focused around health, environment, energy, water supply and local transportation. To this end, the selected communities are organised into 'community organisation (CO)' founded on norms of good governance.

Appropriate support structures are created at various levels to facilitate smooth implementation of the Project. Through networking of local communities, local/regional authorities, private sector and civil societies appropriate fora are established at rayon/oblast level so that they can hold regular dialogue on sustainable development envisioning, mainstreaming of community plans, deciding upon public-private partnership mechanism for implementation of local priorities and carrying out participatory monitoring. Networking of stakeholders at the national level enables overall monitoring and advisory support.

Capacity of duty-bearers in the local communities, local government as well as national level officials is complemented through capacity building activities. Capacity of the COs is built in such a way that they are able to make joint decision with local authorities, mobilize resources, implement local priorities and sustain the result. Capacity of the partners (VC/CC, rayon/oblast etc.) is strengthened in terms of human resources to implement participatory approach propagated by the Project. Training, exposure visits, dialogues and small grants (for community projects), appropriate institutional mechanisms etc. are used as tools for building capacity.

Appropriate management and information systems (MIS) is established to make the stakeholders directly involved in the process of monitoring and assessment of the Project activities. It includes process monitoring, input monitoring, output monitoring and impact monitoring. Flow of information is bottom-up and participatory.

Sustainability of the systems, institutions (community organizations etc.) and services established at local community level under support of the Project is ensured so as not to loose the principles and value propagated by the Project.


1.2 Project Area

CBA Project works in all oblasts of Ukraine and Autonomous Republic of Crimea covering total of 200 rayons (eight in every oblast in average) and will cover 1000 villages/settlements/cities (five in every rayon in average) with population less than 10,000 people.

CHAPTER II



PROJECT ACTIVITIES AND RESULTS

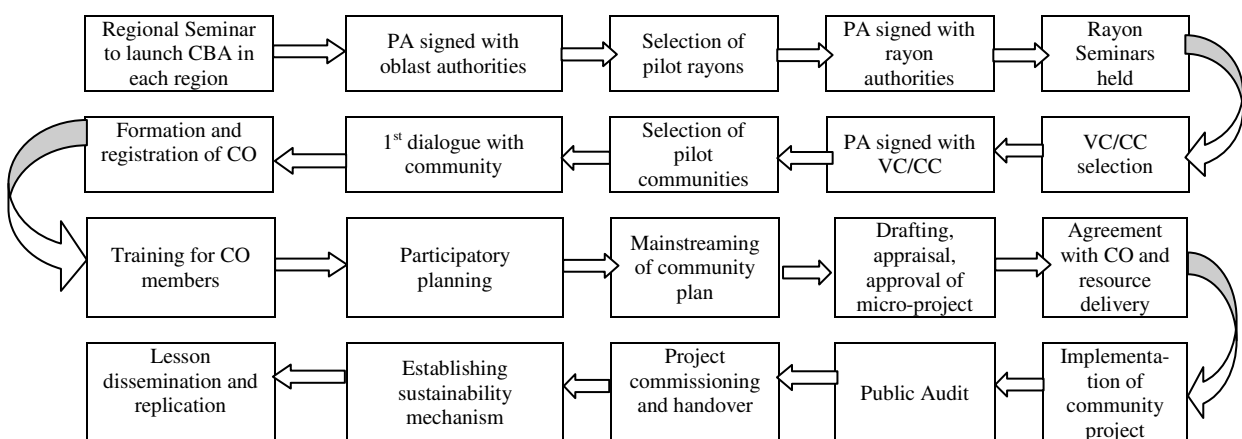

2.1. ESTABLISHMENT OF PARTNERSHIP

2.1.1. Establishment of partnership with regional authorities

Establishment of formal partnership with oblast authorities is considered to be a milestone in CBA implementation. Such agreements are also essential to formalize the role and commitment of the partners (local authorities and UNDP) and to provide an official basis to work with community organizations. Activities of CBA Project in all the regions rely on this partnership which was formalized with 23 oblasts and ARC by signing agreements. In the 2nd quarter, Partnership Agreements were signed with oblast authorities of Odeska and Dnipropetrovska oblasts. As previewed by terms of partnership, premises were allocated by OSA/OC for CBA Oblast Implementation Units/ Community Resource Centres.

2.1.2. Partnership between UNDP and rayons

Selection of pilot rayons and establishment of formal partnership with rayon authorities, through signing of partnership agreement, is considered to be second milestone in CBA implementation. It ensures clear role and commitment of the rayon authorities and provides an official basis to reach village/city councils. To this end, following steps were followed during the quarter.

Since inception, all 200 pilot rayons (and 1 city council) from all the 25 regions of Ukraine were selected for participation in CBA Project. In the reported period, Yampil'skyi rayon of Sum'ska oblast decided to withdraw from participation in the project. It was replaced with Sum'skyi rayon, from reserve list.

In the reported period, 10 partnership agreements were signed by rayons of Odeska and Dnipropetrovska oblast and one PA was terminated in Sum'ska oblast. Totally since inception, 188 agreements were signed by rayons authorities.

2.1.3. Establishing partnership with village / city councils

During the reported period, 149 applications for partnership were received from village/city councils of 15 regions namely AR Crimea, Chernihiv'ska, Dnipropetrovska, Donetska, Kharkiv'ska, Kherson'ska, Kirovohrad'ska, Kyiv'ska, Luhanska, Lviv'ska, Mykolaiv'ska, Odeska, Sum'ska, Zaporizka, Zhytomyr'ska oblasts.

The team of the oblast community resource centre (OCRC) analysed the information of the applications and information received from the respective rayon state administrations. Based on the analysis, they made a ranking of the participating local councils based on the socio-economic hardship and commitment.

The ranked applicants were discussed in 'village/city council selection committee' meetings and 67 local councils were selected as shown in Table-I. Of them, 27 VCs/CCs were substitutes for those 27 VCs/CCs with whom partnership was terminated because (a) either they rejected to continue cooperation or (b) they did not fulfil their commitments. There still remained 6 VCs/CCs to be substituted.

Thus, net addition of VCs/CCs was only 34.

In all cases, the meeting was presided by CBA focal point of Oblast State Administration. Other participants of the meeting included representatives from regional council, rayon state administrations, rayon councils, and CDOs in the oblast.

Local partners were supportive towards methodology offered by CBA as they recognised its value in the local governance and sustainable development. Their opinions are quoted in Box 1.



Photo - 1. Selection of pilot village/city councils in Donetska oblast

Table – I: Selection of Village/City Councils in II Quarter 2009

#	Oblast	No of Rayons	No of applications	No of selected local councils			Substitute VC/CC	No of local councils in reserve		
				VC	TC	CC		VC	TC	CC
1	ARC	2	18	4	0	0	4	0	0	0
2	Chernihivska	1	2	2	0	0	2	0	0	0
3	Dnipropetrovska	1	1	1	0	0	1	0	0	0
4	Donetska	8	76	30	8	2	0	6	2	0
5	Kharkivska	1	14	3	0	0	3	0	0	0
6	Khersonska	2	2	2	0	0	2	0	0	0
7	Kirovohradska	1	1	2	0	0	2	1	0	0
8	Kyivska	0	0	0	0	0	-1	0	0	0
9	Luhanska	4	4	4	0	0	4	0	0	0
10	Lvivska	1	12	1	0	0	1	6	0	0
11	Mykolaivska	1	12	1	0	0	1	0	0	0
12	Odeska	2	3	3	0	0	3	0	0	0
13	Sumska	1	1	1	0	0	1, -6	0	0	0
14	Zaporizka	2	2	2	0	0	2	0	0	0
15	Zhytomyrska	1	1	1	0	0	1	0	0	0
Total		28	149	57	8	2	27, -6*	13	2	0
Cumulative		200	2461	872	103	20	51, -6	532	18	2
Cumulative, %				88%	10%	2%		96%	3%	0%

* 27 VC/CC were selected during II quarter as substitute while 6 terminated partnership but remained without substitute

Total number of pilot local councils amounts to 995 since inception of the Project. Among them, 88% are village councils, 10% town councils and 2% city councils (see Chart 1). Regionwise data about selection of village/city/town councils is given in Annex - I.

Box – 1: Opinions of representatives of Local Authorities about CBA Project

“Heads of village councils are not used to be dictated and controlled by local community. They are used to the old pattern where head of village council is the authority. CBA Project forms a new culture at local level, whereby rights and opinions of local community is taken into account by those who are in power”.

- **O.Sin**, Deputy Head of Zaporizka OSA.

“Participation in CBA Project allows to legalize and institutionalize civil initiatives in small settlements, and creates opportunities for improvement of social infrastructure. Successful experience of participation in CBA will open unlimited opportunities for sustainable development of rural communities”.

- **V.Kruch**, Bolgradska RSA, Odeska oblast

“Before CBA project, people tended to raise only personal issues at community meetings. Now they pay more attention and try to solve issues important for the whole village community. I think this is one of the achievements of CBA Project. People think about the interests of their community, rather than their personal”.

- **V.Sheremeta**, Head of Pereyaslav-Khmelnytska RC, Kyivska oblast.

“Development of territories and empowering local communities is the only way to improve economic situation in villages”.

- **O.Ustynenko**, Head of Department of Internal Affairs, Khersonska OSA.

“Thanks to CBA Project, I realized that I have an efficient team, with the engineer-constructor, good lawyer, very good specialists who can coordinate projects. Our village council is lucky to have many professionals that others don't have”.

- **A.Leybzon**, Head of Muzykivska village council, Khersonska oblast.

“Working together with community, we move ahead of our time. I believe in the strength and wisdom of the community. Together we realized that something really valuable, something that will stay in the memory of generations can be achieved only when there is mutual support, good will and the conviction that we are doing the right thing”.

- **G.Naschuk**, Hostiv village council head, Ivano-Frankivska oblast

“Participation in CBA Project is the possibility to overcome passiveness, build the dialogue between local authorities and communities and initiate the continuous development process”.

- **O.Kirienko**, Deputy Head of Huliaypilska RSA, Zaporizka oblast

In the 2nd quarter 2009, process of signing official terms of partnership with local councils continued. In total, 56 agreements (net 54 only) were signed between CBA and COs of 11 regions. AR Crimea was the most active in this regard, where 12 partnerships were signed (See Table - II).


Total amount of partnerships signed since inception is 599 of the targeted 1000. Signing of ToPs was fast in majority of the regions. It was slow in 8 regions either because the focus was placed more on community aspects of the Project or the Project launching in the rayon/local councils was slow. Regionwise number of agreements since inception is given in Annex – II.

Table – II: Number of ToPs Signed With VCs/CCs During Qr-II

#	Oblast	No. of ToP	#	Oblast	No. of ToP
1	ARC	12	9	Mykolaivska	10
2	Cherkaska	10	10	Rivnenska	2
3	Chernihivska	7	11	Sumska	1
4	I-Frankivska	1	12	Ternopil'ska	1
5	Kharkivska	-1, +1	13	Zakarpatska	5
6	Khersonska	-2	14	Zaporizka	7
7	Luhanska	-4, +4		Total	56, -8, +6*
8	Lvivska	-1, +1		Cumulative	599

* 56 ToPs signed with new VCs/CCs; ToPs terminated with 8 VCs/CCs and 6 ToPs signed with substituted VCs/CCs

Chart –I: Distribution of VC/TC/CC

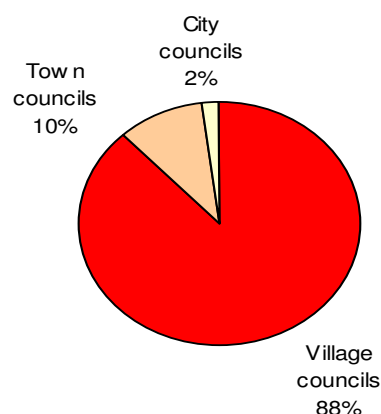

2.2. NETWORKING AND SUPPORT STRUCTURES

To ensure participatory approach in decision-making, appropriate forum is developed at regional and district level. Furthermore, community resource centres are created within framework of oblast and rayon authorities to keep the forums active and effective. Progress on this subject is described in details hereunder:

2.2.1. Project coordination at oblast level

During the quarter, 8 Oblast Coordination Councils (OCC) were formed in 8 oblasts. Since inception, 18 OCCs were formed, in AR Crimea, Cherkaska, Chernihivska, Ivano-Frankivska, Kharkivska, Kirovohradska, Luhanska, Lvivska, Mykolaivska, Odeska, Poltav'ska, Sumska, Ternopil'ska, Vinnytska, Volyn'ska, Zakarpatska, Zaporizka, Zhytomyr'ska oblasts.

During the quarter, 11 sittings of OCC took place. Meetings of these forums focused on following key areas:

- Declaration of OCC formation and approval of its statute
- Hearing of the report on Project implementation in oblast
- Financial commitments of partners
- Support from local authorities to preparation, review and approval of micro-projects.



Photo - 2. Zhytomyr Oblast Coordination Council and Progress Review meeting under the chair of the Deputy Governor of OSA

An oblast coordination council (OCC) is formed under the chair of head/deputy head of OSA/OC and in participation of representatives of local development forums (LDFs), relevant departments, selected VCs/CCs, COs, NGOs and business sector. An OCC coordinates project financing and implementation and participation of national partners; ensures proper awareness of regional and local governments; provides strategic advice on Project implementation and assists in using Project outputs for national strategy and policy development. See Annex – III (a) and III (b) for regionwise details about OCC activity.

CBA management uses the OCC sitting as opportunity to reinforce partnership with local authorities through joint review of progress of project implementation. In the 2nd quarter, 10 OCC sittings were attended by Senior Programme Manager of UNDP and International Project Manager of CBA Project. For details about review meetings see section 2.7.3 and Annex – III (b).

2.2.2. Project coordination at rayon level

Practical cooperation with rayon authorities continues primarily through the mechanism of Local Development Forums (LDF). These forums are established by a decree of rayon administration in each partner rayon. They normally consist of representatives of rayon leadership and heads of relevant units, heads of village councils and CO chairpersons. LDF aims to facilitate dialogue, coordination, planning and decision-making at local level between the oblast and rayon authorities and communities for promoting integration and development. Meetings are held regularly to discuss local development issues such as to mainstream community plans, to support community organizations for technical backstopping and resource mobilization implementation, and handover of community projects.

Key areas of discussions at LDFs are as follows:

- Creation of Rayon Community Resource Centre
- Organization of public audit,
- Assist in improvement of the system of local financing and mobilization of financial resources for community projects
- Help in preparing financial reports for the use of 2nd tranche
- Approve Community Development Plans
- Provide help in technical investigation of the constructions, draft necessary documentation
- Help in preparation of cost-estimate documentation for community projects
- Approve micro-project proposals
- Approve replacement of pilot village councils/communities
- Review progress of CBA implementation in the rayon
- Assist in legal registration of CO

During the quarter LDFs were formed in 35 rayons of 9 oblasts.

Table - III: Rayons with LDF Created in II Quarter 2009

#	Oblast	Rayons with LDF created	
1	Cherkaska	1	Zvenihorodskyi
		2	Talnivskyi
		3	Kanivskyi
		4	Chyhyrskyi
		5	Shpolyanskyi
		6	Umanskyi
		7	Kamianskyi
		8	Horodyschenskyi
2	Chernivetska	1	Putylskyi
		2	Kelmenetskyi
		3	Vyzhnytskyi
		4	Hertsavskyi
3	Dnipropetrovska	1	Pavlohradskyi
		2	Pokrovskyi
		3	Synelnykivskyi
		4	Sofiivskyi
		5	Tomakivskyi
4	Ivano-Frankivska	1	Halytskyi

#	Oblast	Rayons with LDF created	
5	Kharkivska	1	Pervomaiskyi
		2	Novovodolazkyi
		3	Velykoburlutskyi
		4	Zolochivskyi
		5	Izyumskyi
6	Kirovohradska	1	Novoukrainskyi
		2	Malovyskivskyi
		3	Petrivskyi
		4	Svitlovodskyi
7	Lvivska	1	Starosambirskyi
		2	Turkivskyi
8	Mykolaivska	1	Veselynivskyi
		2	Berezhnivatskyi
		3	Yelanetskyi
9	Odeska	1	Artsyzskyi
		2	Kotovskiy
		3	Kodymskyi

Since inception, LDFs were formed in 181 rayons, and 339 sittings were held. Details are presented in Annex - IV.

2.2.3. Rayon Community Resource Centers (RCRC)



Photo – 3. Information board in Kremnetskyi Rayon Resource Centre

Rayon Community Resource Centre (RCRC) is established at the pilot rayon state administration to ensure institutional memory, to coordinate CBA implementation in the rayon and to disseminate information on CBA implementation in the rayon. It is run by the rayon focal person. It may assume informal (with low visibility) or formal status (with high visibility) depending upon the situation.

During the quarter 55 RCRCs were formed in 16 oblasts (Table-IV). Since inception, 93 Rayon Community Resource Centres were formed in 21 oblasts. Luhanska and Kyivska oblasts were most enthusiastic in establishing sustainable RCRCs for conducting further community oriented activities. Details about formation of RCRCs are given in Annex - V.

Table - IV: Rayons with RCRC Created in II Quarter 2009

#	Oblast	Rayons with RCRC created
1	ARC	1 Krasnoperekopskyi 2 Dzhankoyskyi
2	Cherkaska	1 Zvenihorodskyi 2 Talnivskyi 3 Kanivskyi 4 Chyhyrskyi 5 Shpolyanskyi 6 Umanskyi 7 Kamianskyi 8 Horodyschenskyi
3	Chernihivska	1 Shchorskyi
4	Dnipropetrovska	1 Pavlohradskyi
5	Ivano-Frankivska	1 Halytskyi
6	Kharkivska	1 Novovodolazkyi 2 Velykoburlutskyi 3 Pervomaiskyi 4 Izyumskyi
7	Kirovohradska	1 Hayvoronskyi 2 Novoukrainskyi 3 Novomyrhorodskyi 4 Petrivskyi
8	Luhanska	1 Stanychno-Luhanskyi 2 Kreminskyi 3 Antratsyivskyi 4 Popasnyanskyi 5 Svativskyi 6 Bilokurakinskyi

#	Oblast	Rayons with RCRC created
9	Lvivska	1 Zhydachivskyi 2 Buskyi
10	Odeska	1 Kotovskyi 2 Bilhorod-Dnistrovskyi 3 Bolhradskyi 4 Ivanivskyi
11	Rivnenska	1 Sarnenskyi
12	Sumska	1 Krasnopilskyi 2 Lypovodolynskyi 3 Trostyanetskyi 4 Seredyno-Budskyi
13	Volynska	1 Lokachynskyi 2 Ivanychivskyi 3 Kovelskyi 4 Ratnivskyi
14	Zakarpatska	1 Berehivskyi
15	Zaporizka	1 Berdyanskyi 2 Velykobilozerskyi 3 Hulyaipilskyi 4 Novomykolaivskyi 5 Kuibyshevskyi 6 Prymorskyi 7 Polohivskyi 8 Chernihivskyi
16	Zhytomyrska	1 Andrushivskyi 2 Korostyshivskyi 3 Chernyakhivskyi 4 Chervonoarmiyskyi

2.3. ORGANIZING LOCAL COMMUNITIES

Following to selection of village/city councils, steps were taken to select the settlement(s) / local community and mobilize them for concrete action under the framework of CBA Project. Since inception, 963 local communities were organised to work with CBA through following process:

2.3.1. Holding VC/CC level seminars

Orientation was organised in the selected VCs/CCs, individually or collectively, to present CBA Project to the council members, VC/CC-executives, active citizens, NGOs and businesses from the locality.

In perspective of the partnership with oblast and rayon authorities, the seminar focused on sensitizing the local representatives with importance of community-based approach to local development and explaining them the relevant procedure and conditions to achieve concrete results. Participation of the oblast and rayon officials in these local seminars reflected their commitment towards citizens' participation in decision-making process and raised effectiveness of the seminar (Table - V).

In the 2nd quarter, 28 VC/CC level seminars were held in 13 regions. About 760 persons participated in the seminars, including 24 focal persons of CBA project from oblast/rayon level. Since inception, 1006 seminars were conducted in participation of about 23 000 persons. Details on VC/CC seminars are given in Annex - VI.

Table – V: Participation of Regional Officials in the VC/CC Seminars During II Quarter 2009

#	Oblast	No of seminars	No of participants	Participants		
				OSA FP	RSA FP	Leadership /employee of RSA/RC
1	ARC	5	196	0	5	3
2	Cherkaska	1	46	0	0	0
3	Chernihivska	4	78	1	4	4
4	Dnipropetrovska	1	35	0	1	1
5	Ivano-Frankivska	1	38	0	1	0
6	Kharkivska	3	78	0	0	3
7	Kirovohradska	2	39	0	2	0
8	Kyivska	1	17	0	1	0
9	Luhanska	4	79	2	4	11
10	Lvivska	1	14	0	1	1
11	Mykolaivska	2	56	0	1	0
12	Odeska	2	40	0	0	0
13	Zaporizka	1	50	0	1	0
Total		28	766	3	21	23
Cumulative		1006	23041	116	717	771

2.3.2. Selection of local communities

Subsequent to the VC/CC seminar, the participants discussed on the comparative situation of the settlements belonging to the council from the perspective of socio-economic hardship facing them e.g. water supply, health services, energy efficiency, environment and school transportation etc. Based on the ranking, one settlement per VC/CC was selected for CBA Project. Alternative arrangement was made to ensure competition and attract the community which was the most willing and committed to apply self-help approach to resolve their problem.

During the quarter, 24 communities were selected for partnership in 12 Oblasts (Table – VI and VII). They were substituted communities, selected instead of those 25 which were too slow in responding to CBA initiatives or which asked for termination of partnership. Besides, 5 new communities were selected in other oblasts making it a net of 4 communities added on the list. Totally since inception, 47 communities were substituted. Cumulatively, the number of pilot communities reached 963 by end of the second quarter, with 467 communities in reserve list (details in Annex – VII).

Table – VI: Change in Local Communities During II Quarter 2009

SN	Oblast	No. of communities	SN	Oblast	No. of communities
1	ARC	-5, +5	8	Lvivska	-1, +1
2	Dnipropetrovska	-1, +1	9	Mykolaivska	-1, +1
3	Kharkivska	-3, +3	10	Odeska	-2, +2
4	Khersonska	-2, +2	11	Zaporizka	-2, +2
5	Kirovohradska	-2, +2	12	Zhytomyrska	-1, +1
6	Kyivska	-1, +0	Total		- 25, + 24
7	Luhanska	-4, +4	Cumulative		963

Table - VII: Details of Change in Communities by Oblast, in II quarter

SN	Oblast	Rayon	Terminated community	Substituted community
1	AR Crimea	Pervomaiskyi	Pravda	Kormovoe
			Oktyabrskoe	Ostovka
		Kirovskiy	Kirovskiy	Staryi Krym
			Zhuravky	Sinitsyno
		Partyzany	Zolotoe Pole	
2	Dnipropetrovska	Pavlohradskiy	Bohdanivka	Mala Dmytrivka
3	Kharkivska	Bluznyukivskiy	Sofiivka persha	Kirove
			Kryshtopivka	Dobrovillya
			Radhospne	Bashylivka
4	Khersonska	Hornostaivskiy	Velykoblavovishchenka	Zavodivka
		Bilozerskyi	Tomyna Balka	Tokarivka
5	Kirovohradska	Svitlovodskiy	Hlynsk	Myronivka
			Hryhorivka	Ozera
6	Kyivska	Stavyshchenskyi	Antonivka	-
7	Luhanska	Kreminskiy	Borovenky	Novokrasnyanka
		Starobilskiy	Chmyrivka	Shulhinka
		Svativskiy	Kolomychykha	Rudivka
		Popasnyanskyy	Vrublivka	Myrna Dolyna
8	Lvivska	Yavorivskiy	Karachyniv	Chernylyava
9	Mykolaivska	Veselynivskiy	Mykolaivka	Novosvitlivka
10	Odeska	Artsyzskiy	Nadyezhdivka	Ostrivne
		Kotovskiy	Neistota	Zelenyi Kut
11	Zaporizka	Prymorskyi	Preslavske	Novopetrivka
		Berdyanskyy	Mykolaivka	Tersyanka
12	Zhytomyrska	Chernyakhivskiy	Selyanshchyna	Pekarshchyna
	Total	19	25	24

2.3.3. Formation of community organizations



Photo - 4. First dialogue in a community

Pursuant to the community selection, first dialogues were held with the selected communities to sensitize them about importance of collective effort to resolve local development issues in partnership with local authorities and other development agencies including CBA Project (Box - 2).

During the quarter, first dialogue was held in 32 communities of 13 oblasts. In cumulative term, 1015 first dialogues were held with local communities since inception. With this, the level of first dialogue reached more than 100% of the potential minimum target of 1000 first dialogues. It is because some communities need more than one dialogue before they are able to make up their mind to get organized. Additionally, dialogue is needed in the communities which are to substitute the outgoing communities.

Box - 2. Holding Dialogues with Communities

Dialogue is a two-way transparent communication whereby OIU delivers its messages to the participants with logic, facts, figures, pictures and examples (from elsewhere in the country or abroad) while the audience tries to understand relevance of the message into their lives, process to be followed and seek clarification if required. In the CBA Project, at least 4 dialogues are foreseen:

- **Dialogue – I:** is held to familiarise the inhabitants regarding importance of 'organisation, capital and skill' and process of forming community organisation (CO) based on the elements of good governance;
- **Dialogue – II:** is held to familiarise the CO-members with the need and process of participatory planning and bottom-up planning process;
- **Dialogue – III:** is conducted to familiarize the CO-members with the process of establishing accountability, transparency and participatory monitoring;
- **Dialogue – IV:** is carried out to familiarize the CO-members with the concept and process of sustainability of services and benefits

Summarized data on holding dialogues with local communities is given in Table - VIII.

Table – VIII: First Dialogue with COs

#	Oblast	During Q-II	Cumulative	% against target
1	ARC	5	40	100.0
2	Cherkaska	1	42	100.0
3	Chernihivska	2	42	100.0
4	Chernivetska	0	40	100.0
5	Dnipropetrovska	4	43	100.0
6	Donetska	0	0	0
7	Ivano- Frankivska	1	41	100.0
8	Kharkivska	5	47	100.0
9	Khersonska	1	40	100.0
10	Khmelnyska	1	40	100.0
11	Kirovohradska	0	40	100.0
12	Kyivska	1	56	100.0
13	Luhanska	4	45	100.0
14	Lvivska	1	43	100.0
15	Mykolaivska	5	47	100.0
16	Odeska	1	39	97.5
17	Poltavska	0	44	100.0
18	Rivnenska	0	42	100.0
19	Sumska	0	35	87.5
20	Ternopil'ska	0	42	100.0
21	Vinnytska	0	40	100.0
22	Volyn'ska	0	40	100.0
23	Zakarpatska	0	41	100.0
24	Zaporizka	0	44	100.0
25	Zhytomyrska	0	42	100.0

2.3.4. CO formation process and legal forms of COs


As a result of the first dialogues, 65 COs (net 51 only) were formed in the 2nd quarter (see Table - IX) in participation of 19,365 households, which represented 68% of the total households on the CO-territory. The highest percentage of coverage was noted in Khmelnytska and Zakarpatska oblasts (Chart - III). Some of the other regions had reached higher achievement in 2008 itself while some regions were still in the process of community selection and first dialogue. As a result, their progress is seen as lower.

In total, 23,298 persons represented the households to become members of their COs. Of them, 45% were male and 55% were female.

Since inception, 961 CO were formed in all regions of Ukraine except in Donetska. A total of 195712 households participated in the COs.

CO members elected executive (CO-management) team for their respective COs. The CO management team was often balanced in terms of gender with 60% executive members being female (Chart - II). Details on cumulative information on CO formation and other dimensions of COs are given in Annex – VIII.

Chart - II. Gender Balance in CO-MT




In the reported period, 131 Community Organizations got enrolled with VC/CC. Totally, since inception 896 COs enrolled in local government body.

Table – IX: Formation of Community Organisations in II Quarter 2009

#	Oblast	No of rayons involved	No of VC/CC involved	No of COs			No of h/h in community	Participating H/H		CO members			
				Formed	Enrolled with VC/CC	Legally registered		No	In %	Individual members	Associated members	M %	F %
1	ARC	2	5	5	18	12	857	857	100	857	0	45	55
2	Cherkaska	8	40	4	26	30	547	547	100	215	332	45	55
3	Chernihivska	5	6	2	2	4	540	340	63	612	0	41	59
4	Chernivetska	8	10	5	10	0	337	276	82	276	0	55	45
5	Dnipropetrovska	8	40	22	13	14	3191	2373	74	2373	0	58	42
6	Donetska	0	0	0	0	0	0	0	0	0	0	0	0
7	Ivano-Frankivska	1	1	1	4	4	435	348	80	348	0	46	54
8	Kharkivska	5	12	6	13	12	12800	8832	69	786	8046	35	65
9	Khersonska	2	5	0	0	5	0	0	0	0	0	0	0
10	Khmelnitska	1	1	1	2	7	32	32	100	32	0	31	69
11	Kirovohradska	2	10	0	10	9	0	0	0	0	0	0	0
12	Kyivska	1	1	2	2	4	170	121	71	175	0	24	76
13	Luhanska	4	4	4	4	4	373	196	53	234	0	26	74
14	Lvivska	5	21	0	11	8	0	0	0	0	0	0	0
15	Mykolaivska	3	7	5	4	7	585	497	85	693	0	69	31
16	Odeska	4	17	0	0	7	0	0	0	0	0	0	0
17	Poltavska	0	0	0	0	0	0	0	0	0	0	0	0
18	Rivnenska	0	0	0	0	0	0	0	0	0	0	0	0
19	Sumska	0	0	0	0	3	0	0	0	0	0	0	0
20	Ternopil'ska	1	2	0	2	2	0	0	0	0	0	0	0
21	Vinnitska	3	7	7	4	5	8342	4668	56	8041	0	41	59
22	Volynska	0	0	0	0	0	0	0	0	0	0	0	0
23	Zakarpatska	3	5	0	5	4	0	0	0	0	0	0	0
24	Zaporizka	0	0	0	0	0	0	0	0	0	0	0	0
25	Zhytomyrska	1	1	1	1	0	278	278	100	63	215	35	65
	Total	67	195	65*	131**	141***	28487	19365****	68%	14705	8593	45	55
	Cumulative	192	963	961	896	795	267762	195712	73%	178852	56544	41	59

* 14 were formed in replaced communities. New CO formed was 51 only. ** Actual 113 only. 18 registration excluded due to termination of COs. *** 133 only as 8 registration were excluded due to termination of COs. **** Excluding 57344 associated households

Chart - III. Share of Households Participating in COs Since Inception (in percent)

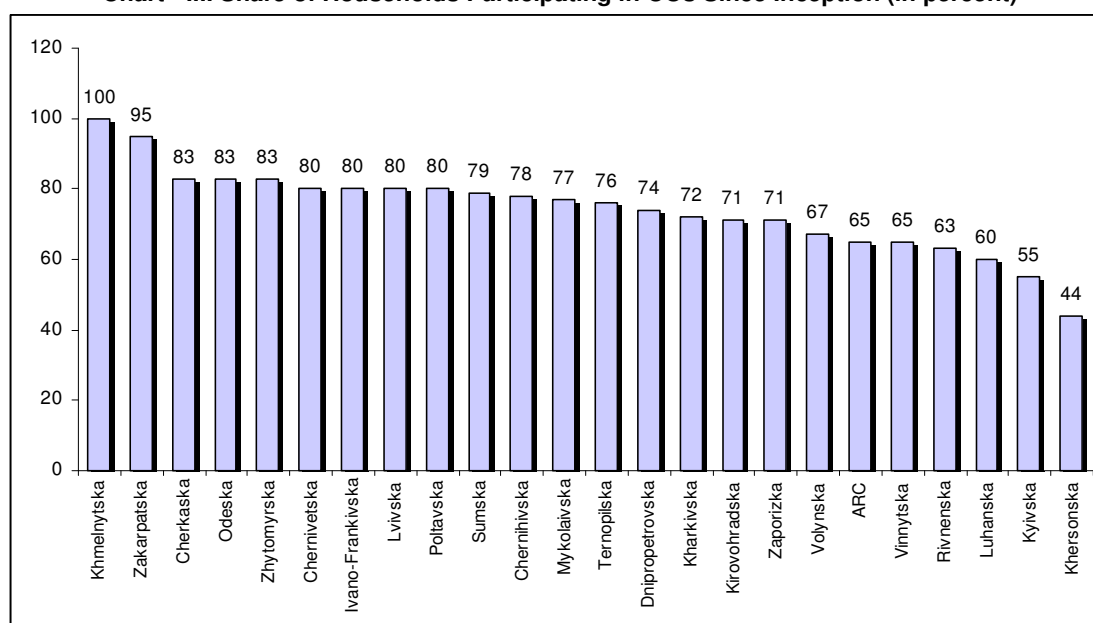

Box - 3. Kindergarten in Bezsal, Poltavska Oblast to Re-open by the Effort of Local Community

Bezsal village (of Lohvytskyi rayon, Poltavska oblast) was chosen as a reserve community, and got the possibility to participate in Project as a substitute of another community whose participation was terminated due to weak response.

Within a short period of time, local community decided to form the community organization "Molodizhna" (meaning "Youth"), consisting of active and energetic people, mostly young and middle-aged, who got united to solve the problems of their living conditions. While other aspects of village life are satisfactory, community suffers a lot from the absence of a kindergarten in the village. There used to be a big kindergarten on the balance of local collective farm, but as it went bankrupt in the early 90-s, the kindergarten was closed down, and the building was repeatedly robbed, and stands unused until now.

As the birth rate in this and surrounding village is recently growing, there is a need to re-open the kindergarten, but the condition of this building is unacceptable: windows are to be replaced, floor and walls need repair, sewage system does not function properly, there is a water pipe passing by but it was never connected to the kindergarten. The abandoned playground and surrounding territory also needs to be put in order.

Community repeatedly tried to solve the problem, but each time the effort was drowning either because of the lack of resources or the lack of instruments that would keep the community united during difficulties and obstacles. When CBA Project offered both, the methodology of community mobilization and the financial support to their initiative, Bezsal village got motivated. Community held the meeting, where local informal leader Ms Galyna Shklyar was selected as head of CO. The organization consists of 53 members but many more people tend to attend the CO meetings. Community established a membership fee, which even non-members were donating for the good purpose. "I sometimes go along the street, - says Galyna, - and people ask if we are still collecting money. Of course, we always do! So we gathered enough to bring the electricity in". Especially active in this regard are the pensioners who put in 20-30 UAH.

In order to solve the problems with maximum efficiency and speed, they are discussed at the general meetings. Community defines its problems and priorities, adopts development plan and establishes membership fee.

However, community's path was not always even. They faced the problem with registration of their organization as legal entity. It was the local state registrar office that refused CO's application, and the issue was then raised at Local Development Forum, and in the media. Rayon authorities provided all the necessary support to the community and finally the community finally got the registration in January 2009.

While functional group of "Molodizhna" was preparing project documentation, local activists did not waste time but organized people to clean the surrounding territory and mend the fence of the playground. The leaking roof was also repaired by community members. At CO's cost, the kindergarten was connected to electricity, and all the wiring inside was replaced. Not only members of CO were engaged in the works, but many others possessing necessary skill gladly helped in making the revival of the kindergarten possible. It is with the help of local citizen that the drainage/sewerage system was retrieved. Documentation and plans of the kindergarten were lost, and there were only hypothetical ideas as of the location of the pipes. It was a local high school pupil equipped with a mine detector who managed to find them. The effort of the united community affected other spheres of Bezsal village life, when part of the road was repaired at the cost of local citizens.

"Molodizhna" is the first to prepare a complex micro-project proposal which was approved in June 2009. While works are going on, community is successful in engaging other sponsors. Director of local agro-firm Oleksiy Kravchenko led the tractor to the CO to dig a trench for water pipe. At the cost of local budget, gas-fired boiler will be installed. Wooden fence for the playground worth about UAH 30.000 will be donated by a sponsor (local forestry enterprise). Local philanthropist Taras Kutoviy has already donated money to the account of CO, and promised to present a TV and music centre for the kindergarten on the occasion of its opening.

Community of Bezsal is thankful to the head of Rayon State Administration Viktor Shchurov and Head of Rayon Council Volodymyr Borysenko who supported communities in the struggle for legal registration, and confirmed their commitment to release co-financing for micro-projects.

With the enthusiasm supported by successful project implementation, and with the new skills of drafting and implementing projects, interacting with local and international donors, and with the authorities, Bezsal community is not going to stop. "Our organization is not limited only to this kindergarten, we'll look for more sources to finance other priorities of our community development plan", says Galyna Shklyar.



Among 961 COs formed since inception, 795 (83%) are already legally registered (Chart - IV). Legal form preferred by most communities for their organizations is *public organization* (90%). The rest is shared by bodies of self-organization of population (5%), cooperatives (2.5%) and associations of co-owners of multi-apartment buildings (2.5%). Distribution of legal forms is visualized in Chart – V.

Chart – IV: Legal Forms of COs





Chart – V: Registration Status of COs



Note: ACMB - association of co-owners of multi-storey building; BSP - bodies of self-organisation of population

Further details on CO formation in the overall period of Project implementation are given in Annexes – VIII, IX.

2.3.5. Organizational maturity

It is important that the CO must reach certain level of maturity before undertaking development task of significant size. To this end, the COs undertake small social/economic/environmental activities of household and community nature during first few months within their own capacity and within the resources available locally.

Most COs implement self-funded initiatives before they receive funding from CBA for their micro-project. Typical cases of such initiatives are: repair works, cleaning the nearby territory, planting trees etc. See Box - 4 for examples of such initiatives.

Box – 4. Examples of Self-funded Community Initiatives Before Achieving Funding From CBA Project

Chernivetska oblast:

- CO *DOHODA* (Mikhalcha village, Storozhynetsky rayon) - improving lighting in the village
- CO *Promin Nadii* (Bernove village Kelmenetsky rayon) - cleaning of the Dnister river banks.
- CO *Dobrobud* (Ozheve village Sokyryansky rayon) - cleaning military cemetery in March 2009 and planting trees in the village in April 2009.
- CO *Perspektyva* (Vashkivtsi village Sokyryansky rayon) - construction of a kindergarten building and improvement of street lighting.
- CO *Dobrobud* (Shebutyntsi village Sokyryansky rayon) - cleaning territory of newly built local health post; cleaning of public park in the village center in April 2009.

Ivano-Frankivska oblast:

- CO *Pikluvalna Rada of Kindergarten Teremok* (Chernyatynska village council in Horodenkivsky rayon) - improving energy saving in their kindergarten (before windows replacement was carried out)

Khersonska oblast:

- CO from Kairy village Hornostaivsky rayon - repairing of a kindergarten and the roof of the local outpatients clinic
- CO from Heroiske village Holoprystansky rayon - repairing of the roof of the village cultural centre
- CO from Rubanivka village Velykolepetysky rayon - partially repaired local outpatients clinic.
- CO from Darivka village Bilozersky rayon - repaired the inside of a local kindergarten.

Kyivska oblast:

- Community from Shaliivka village Skvyrivsky rayon - gasification of the local health post and repair of floor in the school (with support from RSA)

Zaporizka oblast:

- CO *Chapaivske Objednannya Hromadyan* from Polohivsky rayon, Chapaivska village council – carried out village gasification.
- CO *Vladivske Objednannya Hromadyan* from Chernihivsky rayon, Vladivska village council – cleaned waste dump.
- CO *Shans* from Velykobilozersky rayon, Chervona village council - repair of a part of water pipe
- CO *Trudove Objednannya Hromadyan* from Velykobilozersky rayon, Trudova village council – partial repair of water pipe.
- CO *Vidrodzhennya* from Novomykolaivsky rayon, Pidhirnenska village council - replacement of street lighting for energy saving one –

2.4. DEVELOPING CAPACITY

Capacity building is one of the crucial activities of CBA Project. It involves such activities as training, exposure visits, dialogues and various other forms of techniques utilized for skill enhancement/knowledge transfer. The purpose is to enable local communities, local authorities and other partners to adopt and practice the approach promoted by the Project. During the quarter, capacity building activities were focused on communities' representatives and counterparts from local councils. Details on these events are given hereunder:

2.4.1. Training of CBA project staff and national counterparts

(a) Training for CBA staff. During the quarter, training was organized for 2 Finance/Procurement Assistants from Rivnenska and Zaporizka oblasts. Topics of training included:

- UNDP/CBA finance rules and regulations
- Book-keeping in Community Organization
- UNDP tendering procedures
- CO financial reporting on MPP implementation

On 28 April training was organized for drivers of all Oblast Implementation Units. Among topics of the training were:

- Safe driving
- UNDP Insurance Policy
- UNDP rules and procedures for vehicle operation and maintenance

(b) Training for national counterparts.

On 1-3 April, 5 representatives of CBA partners³ participated in training on “Decentralization and Effective Local Self-Government” organized by UNDP Municipal Governance and Sustainable Development Programme under support from the Swiss Agency for Development and Cooperation. Training was organized in Yaremche (Ivano-Frankivska oblast). It brought together mayors and representatives of local councils in order to raise their qualification in the following subjects: local self-government and decentralization, citizens' participation, strategic planning, operational planning, financial planning, social mobilization and establishment of the quality management system for municipal services in accordance with the international standards ISO 9001:2000.



Photo - 5. CBA local partners participating in training on Decentralization and Local Governance

On 10-16 May, study visit to Czech Republic was organized for a group of Ukrainian authorities of national, regional and local level under support of UNDP/Bratislava Regional Centre and Czech Trust Fund (CTF). The main objective of the study tour was to strengthen capacity of the representatives of Ukrainian authorities to undertake pro-active role in promoting participatory governance, sustainable

³

Heads of Lypovodolynsky Rayon Council (Sumська oblast), Novomyrhorodskyi Rayon Council (Kirovohradska oblast), Sofiyskyi Rayon Council (Dnipropetrovska oblast), Deputy Mayor of Rzhyschiv city (Kyivska oblast), Head of Department of Krasnogvardiyskyi rayon, ARC.

energy production and utilization and emergency preparedness. The agenda of the visit successfully combined lectures, field visits and meetings with authorities of national and local level focusing on (a) emergency planning, (b) co-operation between state and local authorities and Dukovany nuclear power plant operators, (c) access to information and (d) involvement of local population in safety arrangement.

The participants greatly appreciated the possibility to meet with their counterparts from Czech ministries, regional administrations and municipalities to learn innovative ways of administration and governance arrangement, and to observe functioning of the Czech system of public administration and governance (Box – 5).

Following eight officials from CBA participated in the study tour:

1	Nadiia Bondarchuk	Ministry of Regional Development and Construction (MRDC)	<i>Deputy Director of Department of Regional Policy</i>
2	Oksana Vetlynska	Secretariat of the Cabinet of Ministers of Ukraine,	<i>Executive officer of Regional Policy Department</i>
3	Dmytro Orlov	Poltavska oblast state administration	<i>HOD, international affairs</i>
4	Viktor Pavlichenko	Cherkaska oblast council	<i>Deputy head</i>
5	Vasyl Baitsym	Volynska oblast state administration	<i>Deputy Head</i>
6	Oleg Obushnyi	Chernihivska oblast council	<i>Deputy Head</i>
7	Mykhailo Popel	Rohatyn rayon council, I-Frankivska oblast	<i>Head</i>
8	Ganna Yatsyuk	EU/UNDP CBA Project	<i>Monitoring and Communications Specialist</i>



Photo - 6. Participants of Study Visit to Czech Republic

Box – 5: Lessons Learnt in CTF Study Visit

The best practices and lessons learnt from the study visit to Czech Republic (CR) for application in Ukrainian context are -

- Czech experience can serve as example for further decentralization and strengthening of local government in Ukraine.
- Energy saving and the more extensive use of alternative sources of energy should become a priority and realized in practice. Leading role in this process should be attributed to local governments. But policies should be elaborated at national level to promote and support creation of the same, based on lessons learnt by CR, whose experience should be taken into account so as to avoid mistakes and inefficiencies.
- Czech experience of introduction of biomass boilers for providing energy/heat to local population can be recommended for introduction in pilot communities of the region.
- Experience of EU/UNDP CBA Project in Rohatynskyi rayon (Ivano-Frankivska oblast) which was presented by Head of Rayon Council Mr. Mykhailo Popel during the study visit should be more extensively used in other regions.

2.4.2. Training for COs

CBA Project offers training and orientation courses for CO-members in following areas –

- 1) CO Management;
- 2) Book-keeping in CO;
- 3) Community planning;
- 4) Drafting MPP.

In the second quarter, a series of financial trainings (Box – 6) was organized for CO treasurers with an aim to strengthen their capacity in financial management of CO and facilitate implementation of community projects. Training agenda included the following topics:

- Book-keeping in community organization;
- Financial reporting to UNDP/CBA in micro-project implementation.

In the reported period, 132 trainings were organized for 3056 representatives of COs and local authorities (see Table - X) to familiarise them with the essence of community-based approach. They learned how to create, register and maintain a community organization; how to write and defend a project proposal, and how to implement an initiative to improve the living quality of local community. Of the total persons trained, 60% were females and 40% were males. Also, 24% of participants were from local authorities (focal points from village/city councils) while 76% of them represented COs.



Photo - 7. Training on CO management in Shpolyansky rayon, Cherkaska oblast

Table – X: Trainings Organised for COs in II Quarter 2009

#	Oblast	No of trainings	Total participants	of Total Participants				of Total Participants			
				Male	%	Female	%	CO-members	%	Local Authorities	%
1	ARC	8	173	113	65	60	35	157	91	16	9
2	Cherkaska	17	407	194	48	213	52	287	71	120	29
3	Chernihivska	3	78	42	54	36	46	64	82	14	18
4	Dnipropetrovska	17	453	157	35	296	65	270	60	183	40
5	Ivano-Frankivska	6	150	51	34	99	66	140	93	10	7
6	Kharkivska	9	221	77	35	144	65	176	80	45	20
7	Khmelnyska	3	67	19	28	48	72	65	97	2	3
8	Kirovohradska	7	178	67	38	111	62	138	78	40	22
9	Kyivska	7	161	45	28	116	72	135	84	26	16
10	Luhanska	7	143	29	20	114	80	94	66	49	34
11	Lvivska	12	240	106	44	134	56	167	70	73	30
12	Mykolaivska	3	92	39	42	53	58	64	70	28	30
13	Odeska	6	71	32	45	39	55	54	76	17	24
14	Rivnenska	4	110	53	48	57	52	78	71	32	29
15	Sumska	9	228	92	40	136	60	152	67	76	33
16	Ternopil'ska	1	5	0	0	5	100	5	100	0	0
17	Vinnytska	2	38	2	5	36	95	38	100	0	0
18	Volynska	8	168	86	51	82	49	159	95	9	5
19	Zaporizka	3	73	21	29	52	71	66	90	7	10
Total		132	3056	1225	40	1831	60	2309	76	747	24
Cumulative		593	14069	5718	41	8351	59	10810	77	3259	23

Totally since inception, more than 14 000 persons from local communities and local governments received training and build up their capacity through 593 trainings organized by CBA Project. About 59% of the trainees were female (see Chart VI) and about 23% belonged to local government institutions (Chart - VII). Details about CBA trainings by oblast are given in Annex - X. In general these trainings were perceived as useful by the participants as reflected by their opinion in Box - 7.

Chart – VI: CO Training Participants by Sex





Chart – VII: CO Training Participants by Institution



Box – 6: Modality of training Package for local communities

In order to achieve the goal and create sustainable 1000 community organizations, capable of carrying out projects, local activists need to receive basic training on technical as well as financial issues. Modality of providing these training to communities included organization of a round of technical trainings (by PMU Engineers) and a round of financial trainings (by CBA Finance/Admin Manager and Finance Assistants) with further decentralization through targeted visits of PMU specialists and consultations provided by Community Development specialists on a regular basis.

Schedule of Finance Trainings Held in 2nd Quarter

27 April - Lviv and Ternopil COs
15 May - Fastiv, for Kyiv oblast COs
4 June - Kharkiv;
5 June - Luhansk;
11 June - Zhytomyr;
12 June - Volyn;
13 June - Rivne;
19 June - Cherkasy and Vinnytsya;
20 June - Kirovograd;
25 June - Dnipropetrovsk;
26 June - Zaporizhya and Khmelnytsky;
29 June - Uzhgorod;
30 June - Ivano-Frankivsk



Photo – 8. Training on financial management for COs in Rivne

Box - 7. CO's Feedbacks on Trainings

«Trainings in «Effective management of community organization», «Participatory Planning» and «Preparation of micro-project proposals» were especially interesting. At these seminars we received methodological recommendations how to manage our organization, form community budget, prepare reports, elaborate micro-project proposals and execute necessary documents» - *Vodyanchuk V.I., Head of CO Pikluvalna rada of kindergarten Zirochka, Horodenkivska town council, Ivano-Frankivska oblast*

«I have received a lot of useful information at trainings in «Participatory Planning» and «Preparation of micro-project proposals» that helped me in solving problems with work with community and in my further work with documents in the framework of the Project». – *Vaselynychuk Z.Z., head of CO Dobrobut, Ivano-Frankivska oblast*

«All trainings were interesting and useful. But I learnt the most at the training in strategic planning and community development. I always try to study and use possibilities to do it. It would be nice if trainings were held not only in rayons for CO leadership, but directly in villages for more CO members. We are interested in having business in a village and in attracting additional resources for the community» *Halyna Biichuk, CO Roksolana, Dovhalivka village, Bilohirsky rayon, Khmelnytska oblast*

«All trainings were interesting, it is impossible to choose one, as all of them are inter-connected. We have learnt a lot about possibilities of communities, believed in possibilities». *Valeriy Poltavchenko, CO Dovira, Honcharivka village, Bilhorod-Dnistrovsky rayon, Odeska oblast*

«...The most interesting trainings were «Management and planning of community activities» and in frames of the training «Preparation of MPP» information about license receiving procedures, approving of project documents, registration of land allotting, etc. As necessary information is almost inaccessible, we are grateful to Zaporizky OIU for the experience gained...» - *Perebyinis Lidiya Mykolaivka, Head of Chapaivske obyednannya hromadyan, Zaporizka oblast*

«I have gained clear idea about the amount of documents necessary for carrying out works on the project; trainings have helped our public organization to improve knowledge of preparing micro-project proposals, participatory planning and effective community management». *Head of CO Vodyansky vodohrai, Vodyane village, Petrivsky rayon, Kirovohradska oblast*

2.5. COMMUNITY DEVELOPMENT PLANS (CDP)

CBA aims to improve living condition of local communities and strengthen participatory governance. For this purpose, it supports participatory planning in the community to enable them to identify local needs; prioritise them based on such criteria as equity, do-ability, sustainability and cost sharing; and get the community priorities mainstreamed into local development plans through joint decision-making process.

2.5.1. Preparation and mainstreaming of community development plan (CDP)

185 second dialogues were conducted during the quarter to initiate participatory planning in the COs. High level of 2nd dialogues took place in Cherkaska, Dnipropetrovska, Kharkivska and Zaporizka oblasts. For other regions, either this stage was already over or just begun (as reflected in cumulative column of Table XI). In regions like Donetsk, the stage is yet to come. In total, 86% of 2nd dialogues were held against the minimum potential target of 1000 (Table - XI):

Table – XI: Second Dialogue with COs

#	Oblast	During Q-II	Cumulative	% of the Target
1	ARC	5	40	100.0
2	Cherkaska	40	40	100.0
3	Chernihivska	2	42	100.0
4	Chernivetska	0	40	100.0
5	Dnipropetrovska	27	27	67.5
6	Donetska	0	0	0
7	Ivano-Frankivska	0	35	87.5
8	Kharkivska	24	28	70.0
9	Khersonska	0	40	100.0
10	Khmelnyska	1	38	95.0
11	Kirovohradska	10	35	87.5
12	Kyivska	2	46	100.0
13	Luhanska	4	45	100.0
14	Lvivska	4	12	30.0
15	Mykolaivska	4	31	77.5
16	Odeska	12	23	57.5
17	Poltavska	0	40	100.0
18	Rivnenska	0	42	100.0
19	Sumska	15	35	87.5
20	Ternopil'ska	3	39	97.5
21	Vinnyska	0	40	100.0
22	Volynska	0	40	100.0
23	Zakarpatska	10	24	60.0
24	Zaporizka	22	38	95.0
25	Zhytomyrska	0	39	97.5
TOTAL		185	859	85.9%

Box - 8. Organized Communities Can Do Much More

Community organization "Development Agency of Stuzhytsia Territorial Community" created under support of CBA Project on 14 November 2008 attracts extra financing from donors for parallel initiatives.

CO decided to develop touristic routes in order to attract more investment to the village and for the benefit of the community. This young organization already managed to complete their first initiative "Stuzhytsia - a pearl of Ukrainian Carpathians". In the framework of this initiative, a touristic route was developed encompassing interesting and unique natural and historic sites of the village. This route is marked throughout the village, and the information brochures are printed. Information about Stuzhytsia and its innovation was widely disseminated through the media and in the internet. Banner was produced and installed at the entrance of the village to advertise touristic potential of the locality and denote major touristic attractions. In the framework of this project, mineral water source and other natural phenomena were examined.

Cost of the project amounted to UAH 45000; it was carried out on the cost of community members under support of scientific institutions and local sponsors. Realization of this project will allow to attract about 2000 tourists and will create additional jobs in the village.

Development of tourism in the village is hindered by the absence of street lighting, this is why community prioritized this problem and suggested it as their initiative for micro-project proposal within the framework of CBA project. Total cost of the project will be UAH 132934.



Photo – 9. CO discussing Community Development Plan, Kruty village of Kodymskyi rayon, Odeska oblast

During the quarter, 220 COs defined priorities of local infrastructure development by compiling community development plans as given in Table - XII. Most communities prioritized energy saving as top priority (45%), followed by medical services (29%) and water supply (21%) as their primary need. Less pressing was the problem of local transportation (3%) and environmental problems (2%). Distribution of priorities among all CDPs of 2nd quarter is visualized in Chart - VIII.

224 COs submitted their priorities to their respective VCs/CCs for approval. Plans concurred by VCs/CCs were then discussed at LDF meetings. Of all the plans discussed, 197 plans were approved by LDFs and recommended for financing (Chart - IX).

Table – XII: CDP Development by COs in II Quarter 2009

#	Oblast	No of COs with CDPs	Priorities of CDPs						No of CDPs reviewed at LDF	No of CDPs approved by LDF
			Health	Water-supply	Energy Saving	Environ-ment	Local Transport	Other		
1	ARC	12	6	3	3	0	0	0	10	0
2	Cherkaska	39	19	6	14	0	0	0	39	39
3	Chernihivska	2	0	1	1	0	0	0	4	12
4	Chernivetska	10	3	0	7	0	0	0	10	7
5	Dnipropetrovska	29	9	7	11	0	2	0	29	0
7	Ivano-Frankivska	5	1	1	3	0	0	0	5	5
8	Kharkivska	27	1	5	19	1	1	0	9	8
9	Khersonska	0	0	0	0	0	0	0	5	2
10	Khmelnitska	1	0	0	1	0	0	0	1	8
11	Kirovohradska	20	1	5	12	1	1	0	20	14
12	Kyivska	2	1	0	1	0	0	0	2	0
13	Luhanska	9	4	2	3	0	0	0	9	11
14	Lvivska	17	7	0	8	1	1	0	17	3
15	Mykolaivska	3	0	0	3	0	0	0	2	2
16	Odeska	16	3	9	4	0	0	0	30	16
18	Rivnenska	0	0	0	0	0	0	0	5	10
19	Sumska	15	3	5	6	0	1	0	9	9
20	Ternopil'ska	3	1	0	1	0	1	0	8	8
23	Zakarpatska	10	4	2	3	1	0	0	10	10
Total		220*	63	46	100	4	7	0	224	197
Percentage		100%	29%	21%	45%	2%	3%	0%		
Cumulative		871	191	165	461	10	44	0	783	636
Percentage		100%	22%	19%	53%	1%	5%	0%		

* 219 only as one CDP was cancelled due to termination of the CO.

Chart – VIII: Priorities of CDPs in II Quarter 2009


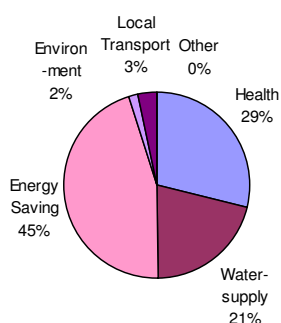


Chart – IX: Share of CDP Reviewed and Approved by LDF in II Quarter

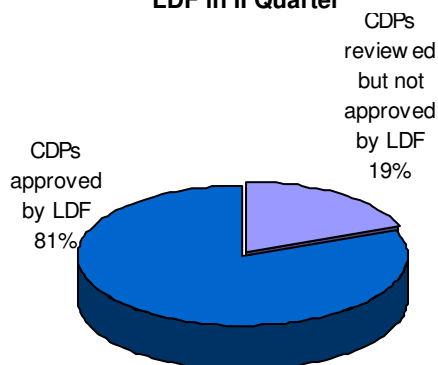

Since inception, 871 CDPs were developed by local communities. According to the existing trend, most of them prioritize energy saving (53%), healthcare (22%) and water supply (19%). 783 of these CDPs were reviewed at LDFs and 636 of them were approved for funding i.e. mainstreamed into local development plan. Details are given in Annexes XI and XII.

2.5.2. Micro-project proposals

Upon approval from LDFs, COs prepared and submitted 190 Micro project proposals (MPPs) to CBA/PMU in 2nd Quarter 2009. The received MPPs went through appraisal, review and approval process at CBA/PMU. A total of 142 micro-project proposals were approved by CBA Project in 2nd quarter. Of the approved MPPs, 57% belonged to energy saving, 20% belonged to health purpose, 18% belonged to water supply and 5% – to local transportation (Table – XIII).

Table – XIII: Number of Micro-projects in II Quarter 2009

#	Oblast	# Appr. MPs	# MPs by typology				
			Health	Energy saving	Water supply	Environment	School bus
1	ARC	2	0	0	0	0	2
2	Cherkaska	0	0	0	0	0	0
3	Chernihivska	5	2	2	1	0	0
4	Chernivetska	9	2	7	0	0	0
5	Dnipropetrovska	0	0	0	0	0	0
6	Donetska	0	0	0	0	0	0
7	Ivano-Frankivska	12	2	10	0	0	0
8	Kharkivska	4	0	3	0	0	1
9	Khersonska	5	2	3	0	0	0
10	Khmelnyska	8	0	4	3	0	1
11	Kirovohradska	2	0	1	1	0	0
12	Kyivska	11	3	7	1	0	0
13	Luhanska	5	4	0	1	0	0
14	Lvivska	1	0	1	0	0	0
15	Mykolaivska	5	0	2	3	0	0
16	Odeska	9	2	2	5	0	0
17	Poltavska	10	0	5	3	0	2
18	Rivnenska	6	0	6	0	0	0
19	Sumska	9	4	2	3	0	0
20	Ternopil'ska	12	1	10	1	0	0
21	Vinnytska	0	0	0	0	0	0
22	Volyn'ska	7	1	5	1	0	0
23	Zakarpatska	5	1	3	1	0	0
24	Zaporizka	8	0	5	2	0	1
25	Zhytomyrska	7	4	3	0	0	0
Total #		142	28	81	26	0	7
Total %		100%	20%	57%	18%	0%	5%
Cumulative #		247	50	144	37	0	16
Cumulative %		100%	20%	58%	15%	0%	7%

Since inception of CBA activities, 247 micro-project proposals were approved by CBA. Most of them are aimed at energy saving (58%) and healthcare (20%). Details on typology of community micro-projects since inception are given in Chart - X. Oblastwise distribution of projects by typology is available in Annex XIII.

Chart – X: Micro-projects by Typology Since Inception

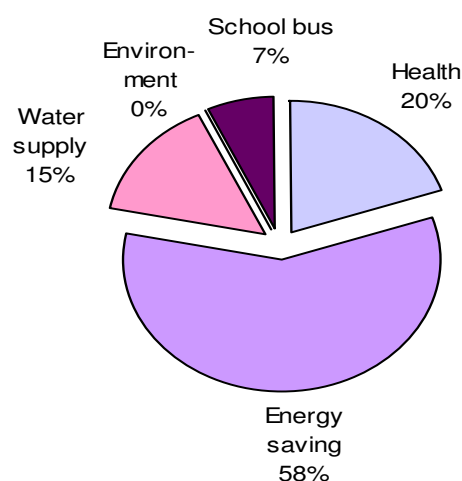


Photo - 10. CO leadership signing agreement with CBA Project (Radisne village, Odeska oblast)


Total cost of all the 247 approved project is about UAH 34.9 mln with an average cost UAH 141 261.5 per micro-project. According to the cost-sharing arrangement, micro-projects will be co-funded by local budget (45%) with 9% contribution from village/city budget, 30% from rayon budget and 6% from oblast budget. Average input of CO is 8% and that of CBA share constitutes 46%. Moreover, communities managed to attract private sector to co-fund their initiatives (1%). Details are given in Table - XIV and Chart - XI.

Table – XIV: Micro-project Proposals Processed Since Inception

(Amount in '000 UAH)

#	Oblast	# App- proved MPs	Total project cost	Cost-Sharing Arrangement						
				CO	CBA	Local Budget				Private Sector
						Sub- Total	VC	RSA	OSA	
1	ARC	9	1 659,3	313,4	471,3	874,6	409,5	465,1	0,0	0,0
2	Cherkaska	0	0,0	0,0	0,0	0,0	0,0	0,0	0,0	0,0
3	Chernihivska	11	1 325,4	106,4	641,2	559,4	140,7	418,7	0,0	18,4
4	Chernivetska	10	1 673,5	137,7	763,3	772,5	10,0	762,5	0,0	0,0
5	Dnipropetrovska	0	0,0	0,0	0,0	0,0	0,0	0,0	0,0	0,0
6	Donetska	0	0,0	0,0	0,0	0,0	0,0	0,0	0,0	0,0
7	Ivano-Frankivska	29	3 709,1	352,8	1 828,6	1 527,6	110,4	1 417,3	0,0	0,0
8	Kharkivska	4	388,7	19,4	194,3	174,9	15,2	159,8	0,0	0,0
9	Khersonska	6	791,4	40,5	391,4	359,5	152,7	206,7	0,0	0,0
10	Khmelnyska	14	1 904,5	160,3	918,6	812,1	91,2	720,9	0,0	13,4
11	Kirovohradska	4	542,8	53,2	244,5	209,3	40,0	149,3	20,0	35,7
12	Kyivska	21	2 825,3	143,4	1 349,1	1 325,5	529,0	796,5	0,0	7,2
13	Luhanska	13	1 702,9	132,7	818,6	624,4	273,3	351,1	0,0	127,2
14	Lvivska	4	561,7	30,7	240,5	289,0	23,7	265,3	0,0	1,5
15	Mykolaivska	8	1 212,0	61,8	599,0	551,2	124,2	427,0	0,0	0,0
16	Odeska	9	1 325,7	110,5	645,1	570,1	41,0	529,0	0,0	0,0
17	Poltavska	11	1 587,7	81,6	764,9	728,5	34,8	389,0	304,7	12,7
18	Rivnenska	17	2 315,3	167,3	1 073,7	1 063,7	292,9	770,9	0,0	10,6
19	Sumska	10	1 683,9	119,9	751,9	812,1	57,1	187,3	567,6	0,0
20	Ternopil'ska	20	2 908,4	359,3	1 302,3	1 189,1	142,0	547,1	500,0	57,7
21	Vinnyska	9	1 210,3	72,4	450,0	684,4	132,5	413,1	138,8	3,5
22	Volyn'ska	12	2 198,3	224,8	862,9	1 110,6	265,7	466,9	378,0	0,0
23	Zakarpatska	6	762,7	44,0	377,1	341,6	40,3	301,3	0,0	0,0
24	Zaporizka	10	1 405,0	75,1	673,0	593,1	126,6	466,5	0,0	63,9
25	Zhytomyrska	10	1 197,7	71,5	600,9	525,4	147,5	377,9	0,0	0,0
Total		247	34 891,6	2 879,0	15 962,1	15 698,7	3 200,4	10 589,2	1 909,1	351,8
In %			100%	8%	46%	45%	9%	30%	6%	1%

Chart – XI: Micro-projects Cost-sharing

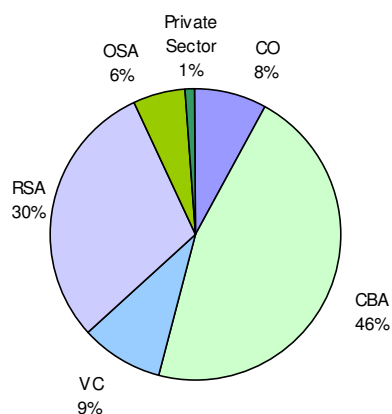

Box – 9: Unified Effort Brings Result

In Zhytomyrska oblast, Community of Vysoke village (Chernyakhivskyi rayon) approved Community Development Plan which prioritizes improvement of medical service delivery. Once organized, community decided to look for opportunities. It was agreed on the meeting to solve the problem of repair works, replacement of windows and doors within CBA micro-project, while purchase of new equipment would be financed from rayon budget.

Community also referred to the Ministry of Healthcare with a request for a new ambulance car. The application was based on the approved Community Development Plan and community's cooperation with CBA Project was quoted. The result of CO's effort did not wait long, and now the ambulance is already driving through the streets of Vysoke village helping those in need. Community takes pride in this achievement and considers it a proof that a united effort brings result.

2.5.3. Beneficiaries of community projects

It is expected that at least 223,202 persons will benefit from the realization of the 247 initiatives on improvement of living quality. Of them, 45% are males, 55% are females. Distribution of beneficiaries by gender and type of project is presented in Chart - XII and Chart - XIII. Genderwise and sectorwise details of beneficiaries are given by region in Annex – XIV and Annex - XV.

Chart – XII: Beneficiaries of Community Projects by Typology since inception


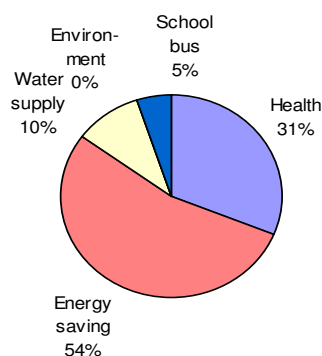


Chart – XIII: Beneficiaries of Community Projects by Sex since inception



Box - 10. Voice of Local Community: Changes Brought About by Participation in CBA Project



Photo - 11. Children can now play in warm rooms of their kindergarten, Ivano-Frankivska oblast

Participation in Community Based Approach to Local Development (CBA) Project teaches rural residents not only professional skills (work with drawings, work on computer, etc.), but also teaches to unite around village and community problems. And one of good examples of such a unity is laying light in Mikhalcha village at the expense of the community, which was carried out beyond the Project realisation.

- **Omelyan Tushynsky**, Deputy Head of public organization DOHODA, Mikhalcha village, Storozhunetsky rayon, Chernivetska oblast

«The community felt its strength in unity, solidarity, felt mutual help from oblast and rayon state administration, rayon council and made sure in the rightness of its choice of village head H.Yu. Naschuk.

– **Melnychuk M.M.**, Head Master of Hostiv secondary school, member of public organization Dobrobut, Ivano-Frankivska oblast

«The community has been organized and mobilised, is assured of itself, shows the initiative, can and wishes to work in future. And we still have a lot of plans...»

- **Nikiforuk N.Yu.**, member of CO Pikluvalna rada of kindergarten Zirochka, Horodenkivska town council, Ivano-Frankivska oblast

«We have started to look at our village in a new manner. Ways to solving problems have changed completely. Instead of 'we should be given' we started to think 'what we can do'; it is observed among villagers of 30-50 years of age».

- **Mykhailo Shevchuk**, CO Dzherelo, Ulashanivka village, Slavutsky rayon, Khmelnytska oblast

«The Project has given a possibility to unite people more, our community is quite active, but we did not know a lot, and now we do know that we can rely not only on ourselves, that there are programmes to help communities, that it is possible to launch cooperation with rayon authorities and get assistance from it».

- **M.D. Okhtanenko**, Head of CO Kairy village (Hornostaivsky rayon, Khersonska oblast)

People became more open. They began to show interest in what is happening and with time they started to trust the CBA Project.

- **Valeriy Poltavchenko**, CO Dovira, Honcharivka village, Bilhorod-Dnistrovsky rayon, Odeska oblast

«...We already think about future, we plan to develop Community Social Center, to put in order a dump, to develop youth movement...»

- **Vasilenko Oleksandr Petrovych**, head of CO Komyshe-zoryanske obyednannya hromadyan, Zaporizka oblast

«Since inception of the CBA Project on our territory the village as though has revived – everybody is expecting changes for the better. Our project is connected with ecology, so villagers are well informed about activities that our community does in frames of the project *Clean Environment*; it even seems that there is less scattered dust on a dump. To reach high European ecology standards, villagers try to adopt and correspond to them, changing personal attitude and aspiring to a civilised way of domestic wastes utilization».

- **Stepan Karpuk**, Head of CO Smolinsky aktiv, urban village Smoline, Malovyskivsky rayon, Kirovohradska oblast



Photo – 12. Young generation will benefit from high level of medical service provision in Krasna Polyana where local ambulatory was repaired and equipped within the framework of CBA Project

2.5.4. Implementation of micro-projects

Financing for micro-project is taken as an opportunity to establish environment of transparency and accountability at local level. Upon approval of the micro-project, an agreement is signed between UNDP and the beneficiary CO for implementation of the micro-project to be done by the CO under a set of terms and conditions that are formed to enhance transparency and accountability. Often media and local authorities are involved while conducting the agreement and third dialogue is held in the community for this purpose. Concept of the third dialogue is given in Box - 2.

During the reporting period a total of 146 third dialogue was held while financing the micro-projects (Table - XV), which is 12.4% of 1175, the minimum potential third dialogues.

Table – XV: Third Dialogue with Cos

#	Oblast	During Q-II	Cumulative	% of the Target	#	Oblast	During Q-II	Cumulative	% of Target
1	ARC	0	7	17.5	14	Lvivska	0	3	7.5
2	Cherkaska	0	0	0	15	Mykolaivska	3	3	7.5
3	Chernihivska	5	7	17.5	16	Odeska	6	6	15.0
4	Chernivetska	0	0	0	17	Poltavska	6	6	15.0
5	Dnipropetrovska	0	0	0	18	Rivnenska	7	15	37.5
6	Donetska	0	0	0	19	Sumska	4	4	10.0
7	Ivano-Frankivska	10	20	50.0	20	Ternopiiska	11	14	35.0
8	Kharkivska	0	0	0	21	Vinnytska	0	10	25.0
9	Khersonska	0	0	0	22	Volynska	4	6	15.0
10	Khmelnyska	7	11	27.5	23	Zakarpatska	3	3	7.5
11	Kirovohradska	5	5	12.5	24	Zaporizka	0	0	0
12	Kyivska	11	15	37.5	25	Zhytomyrska	3	3	7.5
13	Luhanska	8	8	20.0		Total	93	146	12.4

In the 2nd quarter, financing was released for 83 community projects of 18 oblasts, amounting to UAH 1,4 mln. For most projects, it was the 1st tranche released. Since inception, 122 COs received first tranche, 13 COs received 2nd tranche. The total amount disbursed was UAH 2.2 million (Table - XVI).

Table – XVI: Financing of Micro-projects from CBA in II Quarter 2009

#	Oblast	Disbursements			
		1 st Tranche		2nd Tranche	
		No.	UAH'000	No.	UAH'000
1	Chernihivska	5	58,52		
2	Ivano-Frankivska	13	186,72	5	174,6
3	Khersonska	2	28,18		
4	Khmelnyska	1	14,09		
5	Kirovohradska	1	15,14		
6	Kyivska	11	141,80		
7	Luhanska	8	99,01		
8	Lvivska	0	0	2	86,0
9	Mykolaivska	4	63,00		
10	Odeska	1	10,09		
11	Poltavska	1	15,60		
12	Rivnenska	6	88,76		
13	Sumska	2	29,06		
14	Ternopiiska	10	201,89		
15	Vinnytska	0	0	1	35,7
16	Volynska	3	47,66	1	35,7
17	Zaporizka	3	44,73		
18	Zhytomyrska	2	25,98	1	43,4
	Total	73	1 070,23	10	375,3
	Cumulative	122	1 693,44	13	471,7



Photo - 13. Repair of water supply system, Yerkivtsi village of Kyivska oblast



Photo - 14. A parent participates in the repair works after the installation of windows was completed in a kindergarten of Ivano-Frankivsk oblast

Box - 11. Voice of Community: Main Difficulties in Preparation and Realization of Micro-projects

«The main difficulties in preparation and realization of a micro-project are connected with collecting money to Community Project Fund. To solve this problem we had to work much with the community»

– **Kizan H.P.**, Head of CO Vilkhova, Ivano-Frankivska oblast

«It was the first time when we prepared and realized a micro-project, so we had some difficulties with it. Participation in trainings, organized by community development officers, their recommendations helped to cope with the task of the community»

– **Kisilyuk H.**, member of functional group of CO Pikluvalna rada of kindergarten Zirochka, Horodenkivska town council, Ivano-Frankivska oblast

«There is a problem with financing from the budget, we hoped for the rayon, but at the moment it cannot help, we work with people, inform them, work with deputies, but there are still problems, and they should be solved...»

– **L.I.Hanzha**, Head of community organization Novovoznesenske village (Vysokopilsky rayon, Khersonska oblast)

«It is difficult for us to co-finance the project, it was Village Council who had to do it and it did not provide for funds. But we have to go on – people come and bring money and it means that they trust us»

– **H.M. Zelenska**, head of kindergarten Vyshenka, member of territorial community Daryivka village, Bilozersky rayon, Khersonska oblast

«Problems are mainly organizational: general meeting, collecting money... But we cope with them! We inform people more, cooperate with Village Council».

– **Valeriy Poltavchenko**, CO Dovira, Honcharivka village, Bilhorod-Dnistrovsky rayon, Odeska oblast

«...The main problem in preparation of MPP is absence in the community of qualified experts in office equipment, construction norms and others, but the community with the assistance from rayon governmental bodies and Zaporizky OIU overcomes all difficulties...»

– **Mahazeisychkov Andriy Mykhailovych**, Head of Zelenivske Obyednannya Hromadyan, Zaporizka oblast

«Requirements to tender documentation are very rigid. First, it is really difficult to find three contractors, who have necessary licences, certifications, as all of them, especially it concerns our project, are situated on the territory of other oblasts. Second, the amount of tender documentation is quite big and requires certain knowledge and experience in its executing. Specialists from Rayon State Administration and Village Council help us to overcome this difficulty».

– **Alla Ihnatenko**, Treasurer of CO Smolinsky aktiv, urban village Smoline, Malovyskivsky rayon, Kirovohradska oblast

2.5.5. Completed micro-projects

During the quarter, 7 community micro-projects were completed de-facto i.e. all the works envisaged by project documentation are accomplished. De-jure projects are considered completed upon release of the 3rd tranche. During the quarter, one project was completed (school bus). Totally since inception, 7 community projects were completed. (Annex - XVI)

Table - XVII: Completed Micro-projects

#	Oblast	works done	3rd tranche released
1	ARC	2	0
2	Khmelnytska	1	1
3	Lvivska	1	0
4	Ternopil'ska	1	0
5	Vinnitska	2	0
Total		7	1

Box - 12. Opinion of Communities Which Completed Their Micro-projects

«All the best - to children» - this motto was made a reality in our kindergarten Zirochka with implementation of micro-project «Replacement of windows and front door in kindergarten Zirochka Building 1». As we can see the insulation is perfect, design is very nice; windows are simple and easy to use. This is an important factor for energy saving. It is warm and light in the premises now»

– **Basyuk O.O.**, member of CO Pikluvalna rada of kindergarten Zirochka, Horodenkivska town council, Ivano-Frankivska oblast

«The community has solved a pressing problem of energy conservation at school. Now ugly autumn and winter weather is not a problem. Thanks to the Project it will be warm and cozy in classrooms this winter!»

– **O.Sukhorebsky**, Head of CO Pikluvalna rada of Chenykyiv secondary school, Ivano-Frankivska oblast

Box - 13. Community of Krasnaya Polyana Takes Pride in Their Newly Equipped and Repaired Ambulatory

On 23 April 2009 first local community project was inaugurated in Krasna Polyana Village of Krasnohvardiysky rayon, ARC. The community invited representatives from local authorities, Verkhovna Rada of ARC, Secretariat of the Cabinet of Ministers of Ukraine and UNDP Managers to attend the inauguration ceremony.

The guests were impressed with the active position of community members who enthusiastically presented the whole process of micro-project implementation, beginning with the very first steps in self-organization, project preparation and up to its completion. Like most population of rural areas, Krasna Polyana villagers had a vast number of problems: terrible condition of local outpatient clinic, unavailability of kindergarten, problems with field irrigation even though there is Dnipro canal just nearby.



"We decided to do something about it, because waiting for help can last long," says head of local community organization Borys Zahirny. "So we gathered together, decided to create a community organization and finally solve all our problems, one by one. Villagers voted that overhaul and purchase of new equipment for local outpatient clinic is the most pressing problem that needs to be solved in the first place. Community organization then started to collect membership fees, referred to village head for support and started cooperation with CBA Project."

CBA Project team helped to get organized and provided a series of trainings on organizational and financial issues, as well as on preparation of project proposals and project implementation. This was a vital factor that favoured formation and maturity of the community organization.

Head of functional group, who took care of the project implementation process, said that the biggest obstacle at the very beginning was disappointment and passivity of people. *"It was very difficult to convince people in their strength, and that we are able to implement such a project. First funds were raised, and invested. People then realized that a lot depends on their personal participation and started to work more enthusiastically. For instance, after the end of working day, local men were busy purchasing and covering linoleum, villagers made an asphalt path in front of the entrance to the clinic. During this period, our community gathered and invested more than UAH 12 000."*

Village council head supported community initiative and facilitated allocation of about 70% of project cost village budget. UAH 35 000 were given from rayon budget. The CBA Project committed about UAH 45 000 used for purchase of medical equipment and partially for repair works.

Local outpatient clinic staff proudly demonstrated repaired surgeries and new equipment that will make provision of medical services quicker and of better quality. Clinic provides medical services to people from 8 villages of Petrivska v/c. For example, now people can make all the necessary tests urgently and come to rayon hospital physicians only to get diagnosis and recommendations.

Chief doctor of Krasnohvardiysky rayon hospital Mykola Vokhmintsev mentioned: *"This outpatient clinic was in terrible condition: it was cold, dark and very humid in it. People used to freeze here in a few minutes! We are grateful to medical staff who resisted and remained to work here despite terrible conditions, because many physicians simply resigned, and now the problem we have is shortage of qualified medical personnel. But we hope that now there will be numerous professionals willing to work in such an exemplary clinic. Moreover, village head promised to help and guarantee a decent salary."*



Having completed such an important project, *Vidrodzhennya* community organization is going to continue its activities. At a recently held meeting, villagers discussed further priorities of their village development. Votes are divided between re-establishment of a kindergarten and establishing of irrigation system. Given such a split, community decided to collect and count votes in written form.

CO treasurer Valentyna Isupova explained that the community decided to regularly collect membership fee of 3UAH. per month, of which 50 kopecks will go to a special fund to sustain the outpatient clinic in future, i.e. to purchase medicines, equipment, stationary etc.

2.6. COMMUNICATION AND VISIBILITY

Communication, visibility and public relation (PR) activities are designed as a part of Project implementation strategy with a purpose to maximize transparency about the Project activities and to lobby for the cause it aims to promote. Specific activities include media events, media coverage, web portal, communication dissemination, visibility tools etc.

During the quarter, wider public and potential participants were familiarized with Project activities and plans through local media and CBA web site. Visibility of EU and UNDP was assured by each of communication activities. Details of the activities are described below:

2.6.1. Media coverage and media events

In the 2nd quarter, media events changed both in quality and quantity. Alongside with events around launching project activities at different levels and signing partnerships that continued in many regions, there were more targeted media events aimed at familiarizing local journalists with process and results of CBA activities. Among such events are signing of partnership agreements, donor/partner visits, project opening/launching events, joint reviews of CBA progress by local authorities and Project management.



Photo - 15. Senior management of CBA Project interviewed by Odessa regional media



Photo - 16. Mr. Jens Wandel, Deputy Director of UNDP, Regional Bureau for Europe and the CIS interviewed by local journalists during his visit to Yerkivtsi village, Kyivska oblast

During the reporting period, 204 media coverages were registered across Ukraine, including printed and electronic editions, radio and TV reportages (Table - XVIII, Chart XIV). Leading oblasts in this respect were Rivnenska and Ivano-Frankivska oblasts. Oblastwise distribution of media coverages is given Chart - XV.

Box – 14. Project Inauguration in 2nd Quarter

Following micro-projects went through inauguration during 2nd quarter upon their successful completion:

15 April - Inauguration of School bus in Antoniny, Khmelnytska oblast.

23 April - Opening of ambulatory in Krasnaya Polyana village, Krasnogvardiyskiy rayon, ARC (see Box – 13).

23 May - inauguration of school bus for Vyshgorodok community, Ternopil'ska oblast (see Box – 14).



Photo – 17. School bus for Antoniny community, Khmelnytska oblast

Table – XVIII: Media Coverage of CBA Activities During II Quarter 2009

#	Oblast	Total Coverage	SN	Oblast	Total Coverage
1	ARC	7	15	Mykolaivska	7
2	Cherkaska	10	16	Odeska	10
3	Chernihivska	2	17	Poltavska	6
5	Dnipropetrovska	17	18	Rivnenska	18
6	Donetska	1	19	Sumska	5
7	Ivano-Frankivska	23	20	Ternopilska	16
8	Kharkivska	11	21	Vinnytska	4
9	Khersonska	4	22	Volynska	8
10	Khmelnyska	2	23	Zakarpatska	3
11	Kirovohradska	9	24	Zaporizka	11
12	Kyivska	16	25	Zhytomyrska	6
13	Luhanska	4		Total	204
14	Lvivska	4		Cumulative	1209

Chart - XIV. Media Coverage in 2nd Quarter 2009 by Types of Media


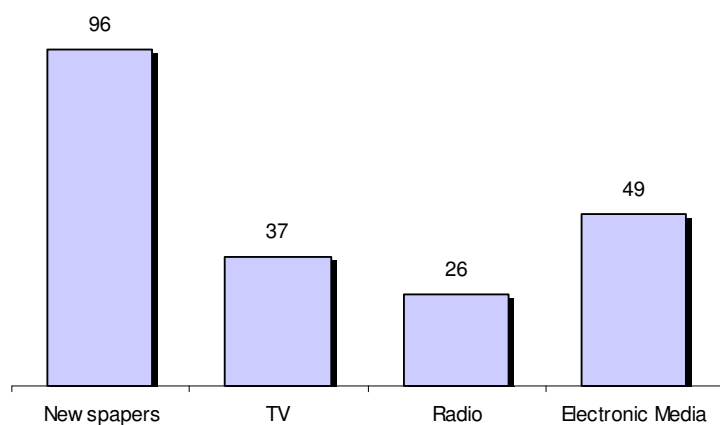


Chart – XV. Media Coverage of CBA Activities During II Quarter 2009

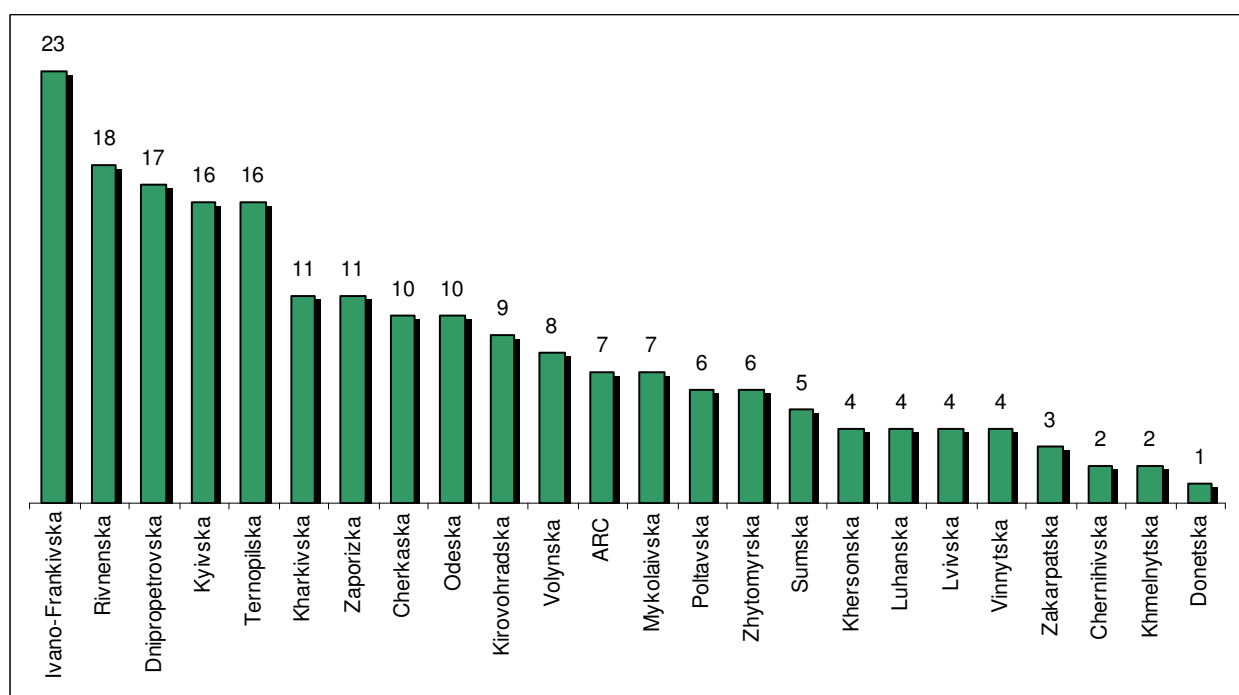

Since inception, media coverage of CBA activities amounts to 1209. Information about total media coverages per region are available in Annex - XVII. Full list of media coverages with brief summaries is available in Annex - XVIII. List and short summary of news publications on partner's web-sites are given in Annex - XIX.

Box – 15: Pupils Gets Easy Access to Their School

On 23 May 2009, the community of Vyshgorodok (Ternopilsky district, Ternopil region) celebrated the completion of their micro-project “School bus”. On this occasion, community organization “Nadiya” decided to invite the high level delegation of donors and local partners to participate in the opening ceremony.

Project opening coincided with Europe Days in Ternopil, and the delegation of high level officials from international organizations and foreign missions to Ukraine gladly accepted community's invitation and came to observe the example of efficient use of donors' funds when multiplied by the effort of local community and cooperation from local authorities. Local Community open-heartedly welcomed the guests among which were: **Mr.Oleksiy Kayda**, Head of Regional Council, **Mr.Ercan Murat** Officer-In-Charge, UNDP Ukraine, **Ms.Joanna Kazana-Wisniowiecka**, Deputy Resident Representative UNDP Ukraine, **Mr.Jose Manuel Pinto Teixeira** Head of the Delegation of the European Commission to Ukraine and Ambassadors of Great Britain and Sweden.

Congratulating the community, Mr. Ercan Murat mentioned that UNDP Ukraine acts with orientation to the human component, such as people's needs, living conditions, expectations about education, social and medical services and life expectancy. *“People should be in the centre of development processes, they should decide what they need, like this particular community did when they defined the school bus as their priority”.*

Mr. Jose Manuel Pinto Teixeira pointed out that *“there is no better way to celebrate Europe Day than to come to this village and participate in the ceremony of inauguration of this Vyshgorodok community school bus. This illustrates most vividly the dimensions of cooperation between the European Union and Ukraine”.*

The project of purchase of the new school bus was implemented with support of EU/UNDP CBA Project (UAH 77 878), Ternopil oblast administration/council (UAH 25 000), Lanovetska rayon administration/council (UAH 52887) and village community organization “Nadiya” which contributed with UAH 7790. Community composed of 255 members started working on this micro-project in August 2008 which was defined as priority by the majority of community members. The school bus will benefit 42 families of 8 villages whose children will now have easier and more comfortable way of transportation to local school.

2.6.2. Participation in external events

With a view of disseminating information about CBA Project among interested target groups, its representatives took part in external events to present the initiative and its modus operandi. In the reported period, Project was presented at 57 external events, including conferences and Europe Days in Zaporizhia and Dnipropetrovsk. CBA Community Development Officers in Dnipropetrovsk oblast also participated in ‘discussion tents’ of Europe Days where they answered the queries of the public about CBA Project and its activities.

2.6.3. Issuing regional newsletter

In order to duly and timely inform local partners/stakeholders as well as participants about progress of CBA activities in the region, a practice of publishing regional newsletters is in place. In the 2nd quarter, OIUs drafted 43 issues of regional newsletter, which was printed and disseminated both electronically (1842 copies) and printed copies (8547 copies), according to the distribution list including oblast administration and council, rayon administration and councils, village councils, local communities, local media and NGOs (see Table - XIX for details). Newsletters were also placed on CBA web site.



Photo – 18. CBA tent at Europe Day in Zaporizhia

Table – XIX: Publication and Dissemination of Regional Newsletters in II Quarter 2009

#	Oblast	Newsletters per II quarter 2009		
		No. of issues published	No. of copies printed & distributed	No. of copies sent electronically
1	ARC	2	125	0
2	Cherkaska	2	150	100
3	Chernihivska	1	90	40
4	Chernivetska	2	200	160
5	Dnipropetrovska	1	100	0
6	Donetska	1	50	75
7	Ivano-Frankivska	3	300	50
8	Kharkivska	3	2110	177
9	Khersonska	0	0	0
10	Khmelnyska	1	100	100
11	Kirovohradska	1	50	50
12	Kyivska	1	55	55
13	Luhanska	2	700	62
14	Lvivska	1	100	8
15	Mykolaivska	1	400	100
16	Odeska	1	200	0
17	Poltavska	1	100	0
18	Rivnenska	2	87	82
19	Sumska	1	1250	10
20	Ternopil'ska	2	190	63
21	Vinnyska	1	200	50
22	Volynska	1	200	100
23	Zakarpatska	1	250	250
24	Zaporizka	3	1770	10
25	Zhytomyrska	1	250	25
Total		36	9027	1567
Cumulative		112	22899	8116

Information about issuance of regional newsletters since inception is available in Annex - XX.

2.6.4. Informing wider public about CBA activities

(a) *Information boards* proved to be an efficient tool of communication of information to local citizen and authorities and ensuring transparency of CBA process. Circular was elaborated and distributed to OIUs, containing recommendations as per installation and content of information boards in oblast and rayon level Community Resource Centres (CRC), but also in village councils and in CO offices (whenever possible).



Photo - 19. Memory board on Local Health Post in Zhytomyrska oblast



Photo - 20. Information board displaying stages and documentation in Zaporizhia Oblast Resource Centre / CBA Implementation Unit

(b) *Database* of CBA pilot communities and approved micro-projects was elaborated and placed on web site. Through this database, it is possible to retrieve each CO profile and all the information about micro-projects (description of the project, cost-sharing arrangement, timeframe, contacts of responsible parties).

(c) *Visibility of partners* is assured by project plaques (temporary) and signboards (permanent) which are produced for each community project site.

2.7 ADVISORY AND MANAGEMENT

Various activities were carried out during the reporting period for effective operation of the Project activities. These activities are reflected in terms of administrative and financial management, coordination arrangement, and monitoring, advisory support and resource mobilisation as described in details hereunder.

2.7.1 Financial delivery

Project expenditure during the quarter reached a total of US \$ 602 920 which was 5.8% of the budget available during that time (Table - XX). Major achievement took place in the area of partnership establishment and project management followed by training and community projects.

Table – XX: Financial Devility by 2nd Quarter (in US \$ '000)

SN	Key Activities	Budget	Project Expenditure			Balance	Delivery %
			Q1	Q2	Total		
1	Training of CBA Project staff and national counterparts on community based approach, project strategy and methodology	149,2	11,1	26,0	37,1	112,1	25%
2	Establish mechanism of participatory planning process at local and regional level	46,0	0,0	0,0	0,0	46,0	0%
3	Support COs for sustainable management and implementation of self-help initiatives (including seed grants)	8 223,0	62,6	190,2	252,8	7 970,2	3%
4	Establish partnership with oblasts & rayons administrations, councils and other local stakeholders (including LDF meetings)	246,7	33,1	67,2	100,3	146,4	41%
5	Effective Project Management	1 633,2	255,9	311,9	567,8	1 065,4	35%
6	PR, Communication and Monitoring Activities	68,5	3,3	7,7	10,9	57,6	16%
TOTAL		10 366,6	366,0	602,9	968,9	9 397,6	9%

2.7.2. Time management

Nation-wide experience of CBA implementation manifests differences between oblasts in terms of time taken to complete each stage of Project implementation. Analysis of time management is given below, indicating time taken in each region to establish partnership, to mobilize communities, to draft and approve micro-project proposals, receive and spend tranches.

2.7.3. Monitoring and review

In order to monitor the progress and quality of CBA process, CBA/PMU Community Development Specialists visited OIU, met local partners and communities, visited project sites. During the quarter, 10 such monitoring visits took place as shown.

One of the objectives of CBA Project is to integrate its methodology in the national process through building capacity of the national partners. It requires that the national partners understand, appreciate and own the process. Joint Review Meetings of CBA implementation in the region could be considered as indicator towards this direction. During the quarter, 10 Review Meetings were held together with oblast authorities. Agenda of such meetings included:

- CBA progress by rayon focal points;
- discussion on challenges and possible solutions;
- strategy for timely completion of project activities;
- elaboration of joint resolutions of key issues.

Details about meetings and summary of recommendations are given in Annex – III (b).

Regional stakeholders may independently review progress of CBA activities in the region, for this the mechanism of Oblast Coordination Council may be used. For details please see chapter 2.2.1.

Table – XXI: Time Taken for Different Action Points (No. of Days) as of May'09**

Oblast	PA Signing	Rayons Selection	VC/TC /CC selection	Community Selection	CO Formation	CO Regist-ration	CDP Approval	Micro Project Approval	First tranche	Second tranche	Total Days***
ARC	66	52	24	42	69	144	58	74	49	33	611
Cherkaska	0	68	35	0	60	26	-	-	-	-	189
Chernihivska	39	0	0	55	47	142	164	6	70	-	523
Chernivetska	90	115	59	0	91	43	132	9	-	-	539
Dnipropetrovska	*	70	57	33	64	45	-	-	-	-	269
Donetska	-	76	-	-	-	-	-	-	-	-	76
Ivano-Frankivska	0	95	61	48	15	58	57	79	98	32	543
Kharkivska	45	0	56	*	102	42	147	33	-	-	425
Khersonska	0	40	51	73	62	80	130	85	54	-	575
Khmelnyska	39	92	37	15	40	82	47	92	80	-	524
Kirovohradska	0	153	45	81	23	32	115	64	70	-	583
Kyivska	76	65	87	34	17	47	35	115	77	-	553
Luhanska	97	86	52	0	83	88	69	119	49	-	546
Lvivska	0	95	34	50	0	107	164	16	96	81	643
Mykolaivska	201	138	49	15	68	44	72	88	60	-	735
Odeska	436	129	53	101	23	31	71	53	-	-	897
Poltavska	0	102	71	67	42	45	82	91	-	-	500
Rivnenska	0	95	49	34	11	72	79	97	84	-	521
Sumska	0	103	82	49	64	34	41	148	-	-	521
Ternopil'ska	0	91	33	45	19	69	79	118	54	-	508
Vinnyska	0	85	36	0	59	44	70	35	39	-	368
Volynska	0	119	30	36	9	59	74	89	93	-	509
Zakarpatska	0	123	55	44	39	45	117	90	-	-	513
Zaporizka	209	134	58	0	62	41	77	91	-	-	672
Zhytomyrska	28	82	42	30	51	60	84	109	45	-	531
Average	58	88	48	37	47	62	89	77	68	49	515

- event not occurred yet

* data is not available


** Day of regional seminar is the starting point and each subsequent action point is counted from the day of previous action;

*** There is overlapping between actions due to simultaneous undertaking of activities. Total number of days, therefore, will be less than shown here.

2.7.4 Manuals

In order to ensure that community mobilization process as well as micro-project implementation are taking place according to CBA methodology, and in order to provide additional guidance support to community organizations, 2 manuals were printed and disseminated through community organizations:

- Manual for Community Organizations (2500 copies)
- Technical Manual (1500 copies).



2.7.5. Donor/partner visits

As CBA progress evolves, the interest of partner agencies and donor increases to observe the efficiency of its implementation. In this context, 6 donor/partner visits were organized during the quarter:



Photo - 21. Officer-In-Charge of UNDP Ukraine, Head of EC Delegation and EU ambassadors visit Vyshgorodok community of Ternopil'ska oblast



Photo - 22. Head of EC delegation and EU ambassadors hosted by Vodiane community, Dnipropetrov'ska oblast



Photo – 23. Mr.Jens Wandel and Mr.Ercan Murat meeting oblast authorities of Luhansk

(a) On 23 April, Mr.Volodymyr Vitka, representative of Secretariat of the Cabinet of Ministers of Ukraine, Department of Regional Policy visited CBA community of Krasnaya Polyana (krasnogvardeyskiy rayon of ARC) and attended opening ceremony of local ambulatory (see Box – 13 for detail).

(b) On 23 May, a delegation composed of UNDP Officer-In-Charge, UNDP Deputy Resident Representative, Head of the Delegation of the European Commission to Ukraine and Ambassadors of Great Britain and Sweden visited inauguration of community project “School Bus” in Vyshgorodok village, Ternopil'ska oblast.

(c) On 24 May, UNDP and EC Delegation senior management visited CBA Kyslyn village, Volyn'ska oblast to meet and interact with local community and observe the status of their micro-project implementation.

(d) On 29 May, Head of EC Delegation to Ukraine and representatives of British, Hungarian, German and Polish visited Vodiane village, Dnipropetrov'ska oblast in order to meet the CBA pilot community and interact with them on the subject of their involvement with CBA Project.

(e) On 18 June Mr. Jens Wandel , Deputy Director, UNDP Regional Bureau for Europe and the CIS and Mr.Ercan Murat, Officer-In-Charge, UNDP Ukraine visited Pereyaslav-Khmelnitskiy rayon to (a) hold the meeting with rayon authorities and (b) to visit Yerkivtsi village, to meet and interact with community organization and observe their project site.


(f) On 20 June, Mr. Jens Wandel, Deputy Director, UNDP Regional Bureau for Europe and the CIS and Mr.Ercan Murat, Officer-In-Charge, UNDP Ukraine visited Luhansk Oblast Implementation Unit/Community Resource Centre of CBA and held meetings with oblast authorities to discuss progress and perspectives of community based projects in the region.

2.7.6. Additional activities

Knowledge Transfer: Support was provided towards promoting community based approach to local development in Ukraine through academia. IPM, Jaysingh Sah, presented a paper on this subject in the workshop organised jointly by UNDP/MGSDP and Academy of Municipal Administration.

Participation in EDM Project: On 6 April 2009 the selection committee assessed 24 applications of the 2nd round participants of all-Ukrainian competition *Every Drop Matters* held by UNDP Ukraine and trademark *Bonakva*, and determined the winners.

According to the criteria mentioned below 14 projects were chosen from following regions: Luhanska (2), Donetsk (1), Mykolaiv'ska (2), Kirovograd'ska (1), Vinnytska (1), Sum'ska (1), Ternopil'ska (1), Ivano-Frankiv'ska (1), Chernigiv'ska (1), Zhytomir'ska (1), Rivnenska (1) and Lviv'ska (1).



CHAPTER III

LESSONS AND FUTURE OUTLOOK

3.1 Stocking the Experience

3.2 Outlook for future

3.1. STOCKING THE EXPERIENCE

Following lessons were learnt during the quarter in course of CBA implementation:

- Oblast authorities are positive to community needs and are willing to supplement with additional fund to be utilized for implementation of community priorities;
- Value of community resource centres is being recognized by oblast/rayon authorities as reflected by increasing demand for strengthening of these centres;
- Technical departments of rayon/oblast are supportive to assist communities in designing/preparation of technical documentation;
- LDF is effective in mainstreaming of community plans and mobilization of local resources (financial as well as human)
- OCC is effective in monitoring of CBA implementation in the oblast, coordination of stakeholders and mobilizing oblast level resources in favour of community based development efforts;
- High level of interest and appreciation has been received from local, district and regional authorities for the results obtained;
- Some regional partners are considering local policy change to make CO- financing possible from state resources;
- Successfully accomplished projects have served as a motivating factor for the communities to look for opportunities to implement their next priority;
- With appropriate advisory support, it is possible to maximize community participation in the process of local development;
- Mindset of local authorities is changing in favour of recognising community priorities as a part of their development plans. However, it will take time for this change across the project area;
- Guidance and support of national partners has proved effective in motivating local stakeholders;
- Physical participation of local/regional authorities in CBA implementation process and political can reach development tasks independently and quickly.
- Rural communities need constant attention and even small stimulating 'victories' for effective unleashing of their potentials.
- In the process of the Project implementation, it appears that there is inadequate institutional structure and financial mechanism oriented to community based local sustainable development and co-financing of international projects
- Co-financing from local budget would be easier to secure if Partnership Agreements between OSA, OC and UNDP envisages compulsory financial share from oblast budget.
- Social mobilization with involvement of local governmental bodies, rayon and oblast administrations/ councils gives high optimism to solve community problems.
- Visibility of community activities and involvement of majority of the community members to work is very important for the overall success of the project.
- Existence of positive examples/success cases of micro-projects and peer to peer learning between COs and other stakeholders at the local level enhances pace and quality of Project implementation at local level.
- Release of first tranche from CBA creates a strong trust and confidence among the COs. Until they receive resource, they tend to remain in illusion and doubt.
- Level of involvement of focal persons in CBA implementation process depends on their regular work load and aptitude to support local communities

Key Challenges and potential threats:

- Global/national financial crisis and reduced state budget resource has posed difficulty in timely cost sharing from local authorities, especially in resource poor region/district;

- In isolated and income-scarce communities, it takes longer time to mobilise resources for cost sharing. It is more so in case of CBA area where the rayons, VCs/CCs and communities are selected based on their poverty and sufferings.
- In situation of budgetary constraint, some oblast authorities find it difficult to meet the costs related with office premises and utilities for their community resource centres
- The process of passing all stages (from priority setting to MPP approval to receiving first tranche to priority implementation) is often felt as long and causes decrease of interest and enthusiasm. Because communities/local stakeholders do not have prior experience on particularities of social mobilisation process and the internal processes of UNDP-led Projects.
- Rural residents are dependent on the cycle of agricultural work. Spring/summer period is a «dead season» in terms of gatherings and collective actions as villagers are busy in agricultural activities. People meet only to solve very pressing and urgent problems.
- Community gains maturity at a slow speed in a step by step manner and through learning by doing process.
- Necessity of quality technical documentation for micro-project proposal preparation require significant amount of money and involve skilled professionals (engineers, builders, people who work on PC, etc.) poses difficulties for the communities which, very often, lack resources and skill. Respective rayon authorities do try to help but they too face the same difficulties from time to time.
- The procedure of payment of the financial documentation is long, sometimes accounts become outdated, even more often prices for goods and services change upward.
- Time limits of the CBA project implementation are tight. But communities often do not realize the limit and tend to proceed according to their own capabilities. However, making them observe this requirement becomes a good stimulating and disciplinary factor.

Opportunities

Opportunity to strengthen rayon level community resource centres for further promotion of CBA methodology;

- Opportunity to expand awareness on CBA methodology through model demonstration;
- Capacity of oblast authorities to supplement fund for co-sharing in community initiatives

3.2 OUTLOOK FOR QUARTER III

Following activities are envisioned for 3rd quarter of 2009:

- Continuation of appraisal, approval and funding of micro-projects
- Enhancing of human resource at local level
- Mid-term evaluation of the CBA implementation
- Oblast level review of the CBA implementation by UNDP/CBA-management
- Documentation of the CBA implementation process
- Holding of Steering Committee meeting
- Effort for resource mobilisation for next phase of CBA
- Organisation of donors' visits
- Exploring mechanism for CO-financing through state budget



Chapter IV.

ANNEXURE

- Annex – I: Selection of Village/City Councils Since Inception**
- Annex – II: Number of Formal Agreements for Partnership with VC/CC Since Inception**
- Annex – III (a): Number of Oblast Coordination Councils and Number of Their Meetings**
- Annex – III (b): Review Meetings Results By Oblast**
- Annex – IV: Local Development Forums Activity**
- Annex – V: Number Full Fledge Rayon Resource Centres**
- Annex – VI: Participation of Regional Officials in the VC/CC Seminar Since Inception**
- Annex – VII: Summary Selection of Local Communities Since Inception**
- Annex – VIII: Formation of Community Organisations Since Inception**
- Annex – IX: Legal Form of COs**
- Annex – X: Number of Trainings for COs Since Inception**
- Annex – XI: CDP Development by COs Since Inception**
- Annex – XII: Priorities of CDPs**
- Annex – XIII: Total Number of Micro-projects by Typology Since Inception**
- Annex – XIV: Beneficiaries of Community Projects Since Inception**
- Annex – XV: Beneficiaries of Community Projects by Typology Since Inception**
- Annex - XVI: Completed Micro-projects Description**
- Annex – XVII: Media Coverage of CBA Activities Registered Since Inception**
- Annex – XVIII: Summary of Media Coverage Per Region**
- Annex - XIX: Summary of News Publications on Partner's Web-sites**
- Annex – XX: Publication and Dissemination of Regional Newsletters**

Annex – I
Selection of Village/City Councils Since Inception

#	Oblast	No of Rayons	No of applications	No of selected local councils			Substituted VC/CC	No of local councils in reserve		
				VC	TC	CC		VC	TC	CC
1	ARC	8	74	35	4	1	8	17	2	0
2	Cherkaska	8	117	39	0	1	0	23	0	0
3	Chernihivska	8	136	33	7	0	2	16	0	0
4	Chernivetska	8	8	38	0	2	0	16	0	0
5	Dnipropetrovska	8	54	38	2	0	3	11	0	0
6	Donetska	8	76	30	8	2	0	6	2	0
7	Ivano-Frankivska	8	150	32	4	4	1	27	0	0
8	Kharkivska	8	111	37	3	0	6	51	0	0
9	Khersonska	8	61	33	7	0	2	29	0	0
10	Khmelnyska	8	165	35	5	0	0	24	0	0
11	Kirovohradska	8	106	37	3	0	2	21	2	0
12	Kyivska	9	148	36	3	1	3, -1	25	0	1
13	Luhanska	8	71	35	5	0	4	23	4	0
14	Lvivska	8	112	33	4	3	3	12	0	0
15	Mykolaivska	8	80	35	5	0	4	36	0	0
16	Odeska	8	87	37	3	0	3	9	3	0
17	Poltavska	8	86	36	4	0	0	15	1	0
18	Rivnenska	8	100	33	5	2	0	21	0	0
19	Sumska	7	87	30	4	1	4, -5	17	0	0
20	Ternopil'ska	8	116	34	6	0	0	27	0	1
21	Vinnytska	8	150	32	7	1	0	14	2	0
22	Volyn'ska	8	117	34	5	1	2	23	1	0
23	Zakarpatska	8	72	35	4	1	0	26	0	0
24	Zaporizka	8	62	36	4	0	2	21	1	0
25	Zhytomyrska	8	115	39	1	0	2	22	0	0
Total		200	2461	872	103	20	51, -6*	532	18	2

* Of total 57 VCs/CCs that terminated partnership, 51 got substituted and 6 still remained to be substituted with new VCs/CCs

Annex – II
Partnership Agreements Signed with VC/CC Since Inception

#	Oblast	Target	No of PA
1	ARC	40	19
2	Cherkaska	40	10
3	Chernihivska	40	21
4	Chernivetska	40	3
5	Dnipropetrovska	40	0
6	Donetska	40	0
7	Ivano-Frankivska	40	40
8	Kharkivska	40	37
9	Khersonska	40	38
10	Khmelnyska	40	28
11	Kirovohradska	40	40
12	Kyivska	41	40
13	Luhanska	40	40
14	Lvivska	40	40
15	Mykolaivska	40	10
16	Odeska	40	0
17	Poltavska	40	40
18	Rivnenska	40	37
19	Sumska	40	35
20	Ternopiiska	40	37
21	Vinnytska	40	11
22	Volynska	40	39
23	Zakarpatska	40	24
24	Zaporizka	40	7
25	Zhytomyrska	40	3
	Total	1001	599

Annex – III (a)
No.of Oblast Coordination Councils and Their Meetings

#	Oblast	Number of OCC	Number of meetings
1	ARC	1	1
2	Cherkaska	1	2
3	Chernihivska	1	1
4	Chernivetska	0	0
5	Dnipropetrovska	0	0
6	Donetska	0	0
7	Ivano-Frankivska	1	0
8	Kharkivska	1	1
9	Khersonska	0	0
10	Khmelnyska	0	0
11	Kirovohradska	1	0
12	Kyivska	0	0
13	Luhanska	1	1
14	Lvivska	1	3
15	Mykolaivska	1	2
16	Odeska	1	1
17	Poltavska	1	0
18	Rivnenska	0	0
19	Sumska	1	1
20	Ternopil'ska	1	1
21	Vinnytska	1	3
22	Volynska	1	1
23	Zakarpatska	1	0
24	Zaporizka	1	2
25	Zhytomyrska	1	1
	Total	18	21

Annex – III (b)
Review Meetings Results By Oblast

Oblast	Decisions and Resolutions
ARC, 23.04.2009	Following the results of the regional meeting the following resolutions are developed. Rayon Councils and Rayon State Administrations should: 1) keep accurately to terms of signed with the CBA Project Partnership Agreements, in particular to consider the problem of assigning funds from local budgets to finance community micro-projects; 2) appoint focal points from Rayon State Administrations and Rayon Councils directly responsible for implementation of the CBA Project in the region
Chernihivska, 25.06.2009	To favour development of newly created communities. Rayon leadership should assist communities in preparing MPP, guarantee co-financing of approved micro-projects.
Dnipropetrovska, 11.06.2009	To favour communities at all levels by providing financial, technical assistance in the CBA Project implementation in the region.
Kharkivska, 16.04.2009	Proceedings decision of the Oblast Coordination Council, decision to create a CRC, co-finance projects.
Luhanska, 15.04.2009	1. To find out reasons for delay in financing by the CBA Project on first signed agreements. 2. To study the question of co-financing MPP either from local or region budgets, or from additional funds of farmers\ households. 3. To hold a seminar for bodies of local self-governance and leaders of community organizations with 5 related OSA departments on coordination of CO micro-projects documents. 4. To plan holding trainings on MPP realization and financial accounting to the CBA Project in april – may 2009 for communities that signed (or that are at the stage of signing) Agreements for co-financing from the CBA. 5. To continue forming first Rayon Community Resource Centers in Stanychno-Luhansky, Svativsky and Antratsyivsky rayons 6. To solve the problem of substituting Rudovsky village council for territorial community from a reserve list. To speed up preparing and submitting on consideration MPP of Kalmykovka and Polovinkino communities 7. To hold additional dialogues with communities from Butovo and Shulhinka villages to mobilize communities and speed up the CBA Project implementation process; 8. To consider at LDF the problem of substituting community from Vyshneve village for one from a reserve list; 9. To hold a dialogue with communities from Maloryazantsevo and Myrnodolyna villages to solve the question of either their further participation in the Project or substituting them for reserve ones; 10. To collect and specify information about micro-projects of community organizations that need co-financing with further solicitation for financial support from the region budget
Mykolaivska, 30.06.2009	To speed up the CBA Project realization and provide any possible help to achieve the Projects objectives
Odeska, 18.05.2009	Decisions: 1. To sign Partnership Agreement between OSA and the CBA Project 2. To solve the problem of equipping the office of oblast community resource centre, 3. To form OCC, 4. To activate preparation of MPP;
Volynska, 24-25.05.2009	1. To acknowledge the readiness of Volyn region leadership to finance 25% of community MPP cost (about 1.5 bln UAH) 2. To consider the possibility of participation in new UNDP Projects 3. To approve the List of micro-projects to co-finance from the region budget. 4. To approve the Order of assigning and using funds from the region budget - subvention to local budgets for micro-project co-financing. 5. Oblast State Administration and Oblast Council should jointly consider the question of assigning additional funds from the region budget to co-finance community micro-projects initiatives.
Zaporizka, 12.06.2009	1. To develop the mechanism of community initiatives co-financing from budgets of all levels. 2. To provide for transfer from the region budget to local budgets amounting 10% of total Project cost.

Annex – IV
Local Development Forums Activity

#	Oblast	Number of LDFs	Number of meetings
1	ARC	8	17
2	Cherkaska	8	10
3	Chernihivska	7	16
4	Chernivetska	8	18
5	Dnipropetrovska	5	2
6	Donetska	0	0
7	Ivano-Frankivska	8	11
8	Kharkivska	5	6
9	Khersonska	8	19
10	Khmelnyska	8	14
11	Kirovohradska	8	12
12	Kyivska	9	9
13	Luhanska	8	24
14	Lvivska	5	12
15	Mykolaivska	8	11
16	Odeska	7	7
17	Poltavska	8	14
18	Rivnenska	8	16
19	Sumska	7	21
20	Ternopil'ska	8	26
21	Vinnytska	8	8
22	Volynska	8	13
23	Zakarpatska	8	15
24	Zaporizka	8	29
25	Zhytomyrska	8	9
	Total	181	339

Annex – V
Number Full Fledge Rayon Resource Centres by Region

#	Oblast	Number of RCRC
1	ARC	6
2	Cherkaska	8
3	Chernihivska	1
4	Chernivetska	1
5	Dnipropetrovska	1
6	Donetska	0
7	Ivano-Frankivska	3
8	Kharkivska	4
9	Khersonska	0
10	Khmelnyska	0
11	Kirovohradska	4
12	Kyivska	9
13	Luhanska	6
14	Lvivska	8
15	Mykolaivska	3
16	Odeska	4
17	Poltavska	0
18	Rivnenska	1
19	Sumska	4
20	Ternopil'ska	1
21	Vinnytska	8
22	Volynska	8
23	Zakarpatska	1
24	Zaporizka	8
25	Zhytomyrska	4
	Total	93

Annex – VI
Participation of Regional Officials in the VC/CC Seminar Since Inception

#	Oblast	No of seminars	No of participants	Participants		
				OSA FP	RSA FP	Leadership/ employee of RSA/RC
1	ARC	47	451	1	42	19
2	Cherkaska	42	601	0	4	3
3	Chernihivska	17	290	1	8	6
4	Chernivetska	40	970	5	15	25
5	Dnipropetrovska	43	571	0	8	10
6	Donetska	0	0	0	0	0
7	Ivano-Frankivska	41	1748	0	40	10
8	Kharkivska	46	831	5	13	35
9	Khersonska	40	1246	1	40	42
10	Khmelnyska	40	330	6	16	37
11	Kirovohradska	42	1547	0	42	55
12	Kyivska	54	1804	0	59	68
13	Luhanska	45	794	9	42	83
14	Lvivska	43	307	1	8	51
15	Mykolaivska	44	1243	0	34	0
16	Odeska	45	755	1	8	6
17	Poltavska	44	882	0	8	13
18	Rivnenska	42	798	14	42	68
19	Sumska	38	856	0	38	29
20	Ternopil'ska	41	604	0	40	15
21	Vinnytska	40	957	2	40	12
22	Volynska	42	748	62	42	66
23	Zakarpatska	43	2379	0	43	43
24	Zaporizka	45	1283	8	45	48
25	Zhytomyrska	42	1046	0	40	27
	Total	1006	23041	116	717	771

Annex – VII
Regionwise Selection of Local Communities Since Inception

#	Oblast	No. of rayons involved	No. of VC/CC involved	No. of communities selected	
				For Partnership	For Reserve
1	ARC	8	40	38	19
2	Cherkaska	8	40	40	23
3	Chernihivska	8	40	40	16
4	Chernivetska	8	40	40	16
5	Dnipropetrovska	8	40	40	11
6	Donetska	0	0	0	0
7	Ivano-Frankivska	8	40	40	27
8	Kharkivska	8	40	47	14
9	Khersonska	8	40	40	29
10	Khmelnyska	8	40	40	24
11	Kirovohradska	8	40	40	21
12	Kyivska	9	40	43	21
13	Luhanska	8	40	40	27
14	Lvivska	8	40	40	12
15	Mykolaivska	8	40	40	36
16	Odeska	8	40	40	12
17	Poltavska	8	40	40	12
18	Rivnenska	8	40	40	21
19	Sumska	7	35	35	17
20	Ternopiiska	8	40	40	28
21	Vinnytska	8	40	40	16
22	Volynska	8	40	40	24
23	Zakarpatska	8	40	40	26
24	Zaporizka	8	40	40	15
25	Zhytomyrska	8	40	40	0
	Total	192	955	963	467

Annex – VIII
Formation of Community Organisations Since Inception

#	Oblast	No of rayons involved	No of VC/CC involved	No of COs			No of h/h in community	Participating H/H		CO members			
				Formed	Enrolled with VC/CC	Legally registered		No	In %	Individual members	Associated members	M, %	F, %
1	ARC	8	40	40	38	33	16434	10602	65	10602	0	46	54
2	Cherkaska	8	40	40	40	39	12893	10701	83	1863	8838	48	52
3	Chernihivska	8	40	38	38	16	3672	2870	78	3495	0	48	52
4	Chernivetska	8	40	40	40	25	3120	2496	80	2496	0	55	45
5	Dnipropetrovska	8	40	39	13	17	3191	2373	74	2373	0	42	58
6	Donetska	0	0	0	0	0	0	0	0	0	0	0	0
7	Ivano-Frankivska	8	40	40	40	40	3400	2624	77	2720	0	37	63
8	Kharkivska	8	46	45	37	33	25318	18219	72	23952	0	36	64
9	Khersonska	8	40	40	40	33	9662	4261	44	7669	0	46	54
10	Khmelnitska	8	40	40	37	34	1732	1732	100	1963	0	32	68
11	Kirovohradska	8	40	40	40	40	3309	2350	71	2455	0	41	59
12	Kyivska	9	41	43	43	41	6023	3304	55	3358	0	40	60
13	Luhanska	8	40	40	38	36	9018	5414	60	6559	0	43	57
14	Lvivska	8	43	40	21	18	7061	5658	80	1492	4166	40	60
15	Mykolaivska	8	40	39	39	35	3451	2830	82	4048	0	43	57
16	Odeska	8	38	38	38	18	17575	14587	83	14587	0	44	56
17	Poltavska	8	40	40	40	40	14814	11925	80	21465	0	43	57
18	Rivnenska	8	40	49	48	44	29574	18666	63	3501	15165	33	67
19	Sumska	7	35	35	35	31	9511	7560	79	7071	489	44	56
20	Ternopiiska	8	40	41	41	41	5442	4135	76	4256	0	38	62
21	Vinnitska	8	38	38	36	32	28885	18674	65	32167	0	41	59
22	Volynska	8	40	40	40	40	8967	6011	67	9615	0	36	64
23	Zakarpatska	8	40	37	37	33	24124	22918	95	3774	19144	30	70
24	Zaporizka	8	40	38	38	38	8153	5478	71	5789	0	44	56
25	Zhytomyrska	8	42	41	39	38	12433	10324	83	1582	8742	37	63
Total		192	963	961	896	795	267762	195712	73%	178852	56544	41	59

Annex – IX
Legal Form of COs

#	Oblast	Legally registered COs	Legal forms of COs				
			ACMB	Cooperatives	BSP	PO	Others
1	ARC	33	8	3	9	12	1
2	Cherkaska	39	0	0	0	39	0
3	Chernihivska	16	0	0	2	14	0
4	Chernivetska	25	0	0	0	25	0
5	Dnipropetrovska	17	0	0	0	17	0
6	Donetska	0	0	0	0	0	0
7	Ivano-Frankivska	40	0	0	0	40	0
8	Kharkivska	33	0	6	0	27	0
9	Khersonska	33	1	1	1	30	0
10	Khmelnyska	34	0	0	0	34	0
11	Kirovohradska	40	0	0	0	40	0
12	Kyivska	41	1	2	0	38	0
13	Luhanska	36	1	0	0	35	0
14	Lvivska	18	0	0	0	18	0
15	Mykolaivska	35	1	3	0	31	0
16	Odeska	18	2	0	12	4	0
17	Poltavska	40	0	4	0	36	0
18	Rivnenska	44	5	0	0	39	0
19	Sumska	31	0	0	0	31	0
20	Ternopiiska	41	0	0	6	35	0
21	Vinnytska	32	0	1	0	31	0
22	Volynska	40	0	0	8	32	0
23	Zakarpatska	33	0	0	0	33	0
24	Zaporizka	38	0	0	0	38	0
25	Zhytomyrska	38	1	0	0	37	0
Total		795	20	20	38	716	1

ACMB - association of co-owners of multi-storey building; BSP - bodies of self-organisation of population;

PO - public/civil society


Annex – X
Number of Trainings for COs Since Inception

		No of trainings	No of participants	Male		Female		Participating CO members		Participating local authorities	
				No.	%	No.	%	No.	%	No.	%
1	ARC	18	374	251	67	123	33	340	91	34	9
2	Cherkaska	25	509	256	50	253	50	336	66	173	34
3	Chernihivska	19	439	224	51	215	49	367	84	72	16
4	Chernivetska	24	491	284	58	207	42	354	72	137	28
5	Dnipropetrovska	17	453	157	35	296	65	270	60	183	40
6	Donetska	0	0	0	0	0	0	0	0	0	0
7	Ivano-Frankivska	29	644	228	35	416	65	593	92	51	8
8	Kharkivska	26	617	223	36	394	64	476	77	141	23
9	Khersonska	24	601	205	34	396	66	407	68	194	32
10	Khmelnitska	28	620	197	32	423	68	470	76	150	24
11	Kirovohradska	21	602	241	40	361	60	455	76	147	24
12	Kyivska	36	1 054	371	35	683	65	787	75	267	25
13	Luhanska	28	626	122	19	504	81	370	59	256	41
14	Lvivska	23	435	190	44	245	56	308	71	127	29
15	Mykolaivska	26	594	239	40	355	60	524	88	70	12
16	Odeska	25	417	188	45	229	55	306	73	111	27
17	Poltavska	24	336	156	46	180	54	283	84	53	16
18	Rivnenska	26	678	259	38	419	62	541	80	137	20
19	Sumska	21	472	209	44	263	56	368	78	104	22
20	Ternopiiska	28	528	202	38	326	62	387	73	141	27
21	Vinnytska	15	736	304	41	432	59	552	75	184	25
22	Volynska	32	818	393	48	425	52	639	78	179	22
23	Zakarpatska	26	520	204	39	316	61	451	87	69	13
24	Zaporizka	27	874	408	47	466	53	755	86	119	14
25	Zhytomyrska	25	631	207	33	424	67	471	75	160	25
Total		593	14069	5718	41	8351	59	10810	77	3259	23

Annex – XI
CDP Development by COs Since Inception

#	Oblast	No of COs with CDPs	Priorities of CDPs						No of CDPs reviewed	No of CDPs approved
			Health	Water-supply	Energy Saving	Environ-ment	Local Transport	Other		
1	ARC	42	11	16	10	1	4	0	30	27
2	Cherkaska	39	19	6	14	0	0	0	39	39
3	Chernihivska	38	11	6	21	0	0	0	40	20
4	Chernivetska	15	4	0	10	0	1	0	15	11
5	Dnipropetrovska	29	9	7	11	0	2	0	29	0
6	Donetska	0	0	0	0	0	0	0	0	0
7	Ivano-Frankivska	40	5	1	34	0	0	0	40	40
8	Kharkivska	39	2	9	25	1	2	0	9	8
9	Khersonska	40	12	6	22	0	0	0	26	8
10	Khmelnyska	40	7	4	24	1	4	0	38	30
11	Kirovohradska	40	3	7	24	1	5	0	40	34
12	Kyivska	47	12	7	27	1	0	0	42	41
13	Luhanska	36	10	10	16	0	0	0	32	36
14	Lvivska	28	11	0	15	1	1	0	28	6
15	Mykolaivska	36	0	6	26	2	2	0	32	32
16	Odeska	30	5	17	8	0	0	0	30	21
17	Poltavska	40	3	21	12	0	4		40	40
18	Rivnenska	42	13	0	24	0	5	0	40	40
19	Sumska	35	9	13	11	0	2	0	34	29
20	Ternopil'ska	39	8	4	23	1	3	0	23	23
21	Vinnyska	35	6	4	19	0	6	0	35	10
22	Volynska	40	4	2	34	0	0	0	40	40
23	Zakarpatska	24	7	2	14	1	0	0	24	24
24	Zaporizka	38	4	14	18	0	2	0	38	38
25	Zhytomyrska	39	16	3	19	0	1	0	39	39
Total		871	191	165	461	10	44	0	783	636
Percentage		100%	22%	19%	53%	1%	5%	0%		

Annex – XII
Priorities of CDPs

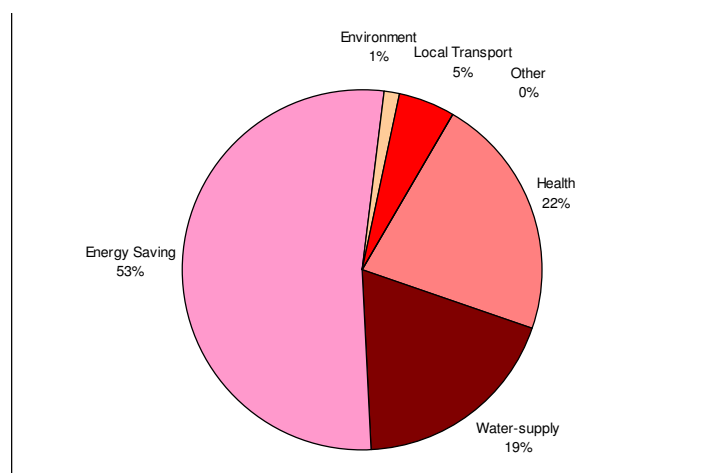

Annex – XIII
Total Number of Micro-projects by Typology Since Inception

#	Oblast	# Appr. MPs	# MPs by typology				
			Health	Energy saving	Water supply	Environment	School bus
1	ARC	9	2	0	5	0	2
2	Cherkaska	0	0	0	0	0	0
3	Chernihivska	11	3	6	2	0	0
4	Chernivetska	10	2	7	0	0	1
5	Dnipropetrovska	0	0	0	0	0	0
6	Donetska	0	0	0	0	0	0
7	Ivano-Frankivska	29	4	25	0	0	0
8	Kharkivska	4	0	3	0	0	1
9	Khersonska	6	3	3	0	0	0
10	Khmelnyska	14	0	8	3	0	3
11	Kirovohradska	4	0	2	1	0	1
12	Kyivska	21	5	14	2	0	0
13	Luhanska	13	6	5	2	0	0
14	Lvivska	4	2	2	0	0	0
15	Mykolaivska	8	0	5	3	0	0
16	Odeska	9	2	2	5	0	0
17	Poltavska	11	0	5	3	0	3
18	Rivnenska	17	4	13	0	0	0
19	Sumska	10	4	2	3	0	1
20	Ternopil'ska	20	2	16	1	0	1
21	Vinnyska	9	0	6	1	0	2
22	Volynska	12	2	9	1	0	0
23	Zakarpatska	6	2	3	1	0	0
24	Zaporizka	10	0	5	4	0	1
25	Zhytomyrska	10	7	3	0	0	0
Total		247	50	144	37	0	16
Percent		100%	20%	58%	15%	0%	7%

Annex – XIV
Beneficiaries of Community Projects Since Inception

#	Oblast	# Approved MPs	No of beneficiaries		
			Total	M	F
1	ARC	9	2556	1119	1437
2	Cherkaska	0	0	0	0
3	Chernihivska	11	7758	4152	3606
4	Chernivetska	10	11285	4924	6361
5	Dnipropetrovska	0	0	0	0
6	Donetska	0	0	0	0
7	Ivano-Frankivska	29	47901	20223	27678
8	Kharkivska	4	2572	1085	1487
9	Khersonska	6	10534	4980	5554
10	Khmelnyska	14	6187	2386	3801
11	Kirovohradska	4	3069	1361	1708
12	Kyivska	21	11895	4734	7161
13	Luhanska	13	9923	4932	4991
14	Lvivska	4	2444	1035	1409
15	Mykolaivska	8	5640	2443	3197
16	Odeska	9	11273	4270	7003
17	Poltavska	11	4707	2032	2675
18	Rivnenska	17	16949	9115	7834
19	Sumska	10	7224	3392	3832
20	Ternopil'ska	20	9375	4239	5136
21	Vinnytska	9	12543	5681	6862
22	Volynska	12	10209	4553	5656
23	Zakarpatska	6	9401	4131	5270
24	Zaporizka	10	10720	4645	6075
25	Zhytomyrska	10	9038	4641	4397
	Total	247	223203	100073	123130
	Percent		100%	45%	55%

Annex – XV
Beneficiaries of Community Projects by Typology Since Inception

#	Oblast	# Approved MPs	No of beneficiaries					
			Total	Health	Energy saving	Water supply	Environment	School bus
1	ARC	9	2556	822	0	1328	0	406
2	Cherkaska	0	0	0	0	0	0	0
3	Chernihivska	11	7758	5374	1978	406	0	0
4	Chernivetska	10	11285	8922	1561	0	0	802
5	Dnipropetrovska	0	0	0	0	0	0	0
6	Donetska	0	0	0	0	0	0	0
7	Ivano-Frankivska	29	47901	2514	45387	0	0	0
8	Kharkivska	4	2572	0	1855	0	0	717
9	Khersonska	6	10534	9871	663	0	0	0
10	Khmelnyska	14	6187	0	3851	536	0	1800
11	Kirovohradska	4	3069	0	2243	290	0	536
12	Kyivska	21	11895	5252	5223	1420	0	0
13	Luhanska	13	9923	5330	4082	511	0	0
14	Lvivska	4	2444	1695	749	0	0	0
15	Mykolaivska	8	5640	0	3893	1747	0	0
16	Odeska	9	11273	6984	1364	2925	0	0
17	Poltavska	11	4707	0	2107	1555	0	1045
18	Rivnenska	17	16949	4359	12590	0	0	0
19	Sumska	10	7224	3756	2692	296	0	480
20	Ternopilska	20	9375	859	7692	217	0	607
21	Vinnyska	9	12543	0	5906	1902	0	4735
22	Volynska	12	10209	1483	8353	373	0	0
23	Zakarpatska	6	9401	4922	3319	1160	0	0
24	Zaporizka	10	10720	0	3676	6630	0	414
25	Zhytomyrska	10	9038	7552	1486	0	0	0
	Total	247	223203	69695	120670	21296	0	11542
	Percent		100%	31%	54%	10%	0%	5%

Annex – XVI
Completed Micro-projects Description

#	Oblast	N	Description
1	ARC	1	Repair and equipment of ambulatory in Krasna Polyana, Krasnogvardiyskiy rayon
		2	Repair of water supply system in Zvezdnoe village, Krasnogvardiyskiy rayon
2	Khmelnyska	1	School bus in Antoniny, Krasylivskiy rayon
3	Lvivska	1	Repair of Local Health post in Arlamivska Volya, Mostyskiy rayon
4	Ternopilska	1	School bus for Vyshgorodok, Lanivetskiy rayon
5	Vinnyska	1	School bus in Floryno, Bershadskiy rayon "
		2	School bus in Severynivka, Zhmerynskiy rayon
	Total	7	

Annex – XVII
Media Coverage of CBA Activities Registered Since Inception

#	Oblast	No. of Coverage	Media Coverage				Partners' web sites
			News-papers	TV	Radio	Electronic Media	
1	ARC	33	19	1	0	13	13
2	Cherkaska	29	13	5	3	8	7
3	Chernihivska	22	3	2	5	12	12
4	Chernivetska	18	5	5	3	5	5
5	Dnipropetrovska	41	23	11	2	5	6
6	Donetska	1	1	0	0	0	0
7	Ivano-Frankivska	44	27	4	1	12	23
8	Kharkivska	149	60	27	7	55	31
9	Khersonska	33	26	2	0	5	11
10	Khmelnyska	21	12	5	3	1	16
11	Kirovohradska	46	45	0	1	0	30
12	Kyivska	81	41	24	9	7	7
13	Luhanska	27	18	5	3	1	16
14	Lvivska	36	23	0	1	12	14
15	Mykolaivska	18	9	3	2	4	11
16	Odeska	36	15	8	0	13	19
17	Poltavska	32	15	4	5	8	10
18	Rivnenska	130	48	16	37	29	28
19	Sumska	60	18	3	24	15	25
20	Ternopil'ska	91	24	23	23	21	20
21	Vinnytska	35	8	4	2	21	21
22	Volyn'ska	47	9	11	8	19	17
23	Zakarpatska	28	22	2	0	4	3
24	Zaporizka	78	60	12	6	0	14
25	Zhytomyrska	73	27	17	18	11	11
Total		1209	571	194	163	281	370

Annex – XVIII
Summary of Media Coverage Per Region (in Ukrainian)

ARC

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Вперед"	Объявления о проведении тендеров в Первомайском районе	14.03.2009	Объявления о проведении тендеров в Первомайском районе
2	"Огни маяка"	Первые результаты партнерства	25.04.2009	Торжественное открытие проекта ОГ "Ремонт и оборудование амбулатории в с. Красная поляна"
3	"Крымские известия"	"Громада всему голова"	13.04.2009	Торжественное открытие проекта ОГ "Ремонт и оборудование амбулатории в с. Красная поляна"
4	"Вперед"	Объявления о проведении тендеров в Первомайском районе	22.06.2009	Объявления о проведении тендера на закупку школьного автобуса в Первомайском районе
5	"Сакская газета"	Объявления о проведении тендеров в Первомайском районе	14.05.2009	Объявления о проведении тендера на закупку школьного автобуса в Сакском районе
6	"Присивашье"	Объявления о проведении тендеров в Первомайском районе	15.05.2009	Объявления о проведении тендера на закупку школьного автобуса в Советском районе
Телевізійні репортажі				
1	ГТРК Крым	Открытие амбулатории в селе	23.04.2009	Торжественное открытие проекта ОГ "Ремонт и оборудование амбулатории в с. Красная поляна"

CHERKASKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Шполянські вісті"	Громади затверджують плани розвитку	19.06.2009	про ФМР
2	РРГ "Трудова Слава"	Сільські громади готують проекти	15.06.2009	про засідання ФМР
3	Чигиринські вісті	Громади звітуються	12.06.2009	Засідання ФМР
4	Чигиринські вісті	Разом дієвіше	10.05.2009	про навчання для ОГ
5	Днірова зірка	Результати впровадження проекту СВА	квітень	про хід реалізації проекту
6	"Шполянські вісті"	продовження впровадження проекту "Місцевий розвиток, орієнтований на громаду"	20.04.2009	про результати проекту на даному етапі
7	Шевченків край	проект "Місцевий розвиток, орієнтований на громаду" на Звенігородщині - про впровадження проекту	06.05.2009	про результати проекту на даному етапі
8	Вісник Городищини	Міжнародна співпраця - шлях до добробуду	28.05.2009	про навчання громад
9	Уманська зоря	на підтримку місцевих громад	24.06.2009	Засідання ФМР
Телевізійні репортажі				
1	Шполянський телеканал	Новини: про форум місцевого розвитку - результати форуму	19.06.2009	про ФМР

CHERNIHIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Деснянська правда"	"Підписання угод до фінансування ПРООН "	14.04.2009	Обласна газ.- 4 громади підписали угоди з ПРООН.
Телевізійні репортажі				
2	Обласне телебачення	Підписання угод до фінансування на обласному рівні. "	13.04.2009	Підписання угод до фінансування на обласному рівні. "

DNIPROPETROVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Рідний край"	"Місцевий розвиток орієнтований на громаду"	03.04.2005	У Межиріччі закінчився другий етап
2	"Вісті Софіївщини"	"Вік живи - вік учись"	14.05.2009	Про делегацію Дніпропетровського району на Софіївщину
3	"Вісті Софіївщини"	"Побували у Водянічів Евросоюзівці"	06.06.2009	
4	"Зоря"	"Побували у Водянічів Евросоюзівці"	05.06.2009	
5	"Зоря"	"Підписан Угода між ПРООН та Дніпропетровською Обласною Радою"	13.06.2009	
6	"Рідний край"	"Підписана Угода між ПРООН та Дніпропетровською Обласною Радою"	19.06.2009	Павлоград. Район в цілому та 6 територ. Громад були учасниками підписання Угоди між ПРООН та Дніпропетровською Обласною Радою
7	"Голос України"		20.06.2009	
Телевізійні репортажі				
1	51 Державний канал	Новини	11.06.2009	
2	27 канал	Новини	11.06.2009	
3	34 канал	Новини	11.06.2009	
4	9 канал	Новини	11.06.2009	
5	11 канал	Новини	11.06.2009	
6	Криворізьське ТБ	Новини	29.05.2009	
Радіо репортажі				
1	Криворізьське радіо		03.06.2009	Щодо впровадження Проекту ЕС/ПРООН СВА у Софіївському районі
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОП/РДА/РР/СВА)				
1	www.tri-sector.org.ua	партнерство Дніпропетровської обласної ради з ПРООН	14.06.2009	оглядова зустріч в Дніпропетровській області
2	www.civicua.org – Громадський простір	партнерство Дніпропетровської обласної ради з ПРООН для покращення життя сільських громад	16.06.2009	оглядова зустріч в Дніпропетровській області

DONETSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				

1	"Новая жизнь" (Старобешеве)	На границу надейся, а сам не плошай	06.05.2009	
---	--------------------------------	--	------------	--

IVANO-FRANKIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Злагода	Сила громади - у єдності	02.05.2009	Про затвердження МПП 5 громад Тлумачького району, підписання угоди ОГ та СВА, оголошення тендеру на виконання РБР
2	Кутищенські вісті	Робота громадської організації	02.04.2009	Про діяльність громадської організації "Відродження Кутищенського краю"
3	Край	Є стимул до подальшої співпраці	08.05.2009	Про проведення круглого столу на тему звітування за використані кошти проекту, виконання робіт на об'єктах
4	Голос Опілля	В Чехію - за досвідом	23.05.2009	Про візит голови Рогатинської РР Чеської республіки в рамках проекту СВА
5	Рогатинська земля	Ми працюємо на перспективу	30.05.2009	Про прес-конференцію для журналістів Рогатинського району голови Рогатинської РР в Республіку Чехія
6	Голос Опілля	II Форум місцевого розвитку Рогатинського району	30.05.2009	Про проведення засідання II Форуму місцевого розвитку Рогатинського району
7	Голос Опілля	Завершення однієї справи - початок іншої	06.06.2009	Про звітування громад за засіданні ФМР про проведену роботу . Публікація резолюції ФМР
8	Рогатинська земля	Рогатинщина - пілотний район і лідер впровадження проекту ЄС/ПРООН	06.06.2009	Про стан реалізації проекту "Місцевий розвиток, орієнтований на громаду" в 5 громадах рогатинського району
Телевізійні репортажі				
1	ТБ "Захід"	Прес-конференція голови Рогатинської районної ради про візит в Чеську республіку	30.05.2009	Прес-конференцію для журналістів Рогатинського району голови Рогатинської РР в Республіку Чехія
Радіо репортажі				
1				

Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	http://pravda.if.ua/news-7090.html	«Місцевий розвиток, орієнтований на громаду»	02.04.2009	2 квітня 2009р. в приміщенні Івано-Франківської ОДА відбулось урочисте підписання Угод про партнерство між трьома громадами Тлумацького району та Проектом «Місцевий розвиток, орієнтований на громаду» (СВА), який фінансується Європейським союзом (ЄС), співфінансується та впроваджується Програмою розвитку ООН в Україні (ПРООН) в Івано-Франківській області.
2	http://odtrk.if.ua/category/peredachi/%D0%BC%D0%B5%D1%80%D0%B8%D0%B4%D1%96%D0%B0%D0%BD/	“На Європейських меридіанах” – автор Ольга Котюк	08.04.2009	Міський голова Тлумаця Михайло Ковбас веде мову про хід в районі проекту ЄС/ПРООН „Місцевий розвиток, орієнтований на громаду”.
3	http://planet.if.ua/economic/367-miscevij-rozvitok-orijentovani-na-gromadu.html	Місцевий розвиток, орієнтований на громаду»	03.04.2009	2 квітня 2009р. в приміщенні Івано-Франківської ОДА відбулось урочисте підписання Угод про партнерство між трьома громадами Тлумацького району та Проектом «Місцевий розвиток, орієнтований на громаду» (СВА), який фінансується Європейським союзом (ЄС), співфінансується та впроваджується Програмою розвитку ООН в Україні (ПРООН) в Івано-Франківській області. Ці угоди закріплюють обов'язки партнерів щодо спів-фінансування проектів громад, які вирішили само-організуватись і покращити свої умови проживання
4	http://zik.com.ua/ua/news/2009/04/03/175925	У школах Тлумацького району мінятимуть вікна за гроші Євросоюзу	03.04.2009	Три громади Тлумацького району стали учасниками проекту Європейського Союзу «Місцевий розвиток, орієнтований на громаду» (СВА) і підписали угоди про співфінансоване партнерство. Проект передбачає заміну старих вікон у школах районів на металопластикові. Про це 3 квітня власкора ЗІКу повідомили у прес-службі Івано-Франківської облдержадміністрації
5	http://vezha.org/news/13823.html	Три громади Івано-Франківській області підписали Угоди про партнерство з Проектом ЄС/ПРООН «Місцевий розвиток, орієнтований на громаду»	02.04.2009	Три громади Тлумацького району стали учасниками проекту Європейського Союзу «Місцевий розвиток, орієнтований на громаду» (СВА) і підписали угоди про співфінансоване партнерство. Проект передбачає заміну старих вікон у школах районів на металопластикові. Про це 3 квітня власкора ЗІКу повідомили у прес-службі Івано-Франківської облдержадміністрації
6	http://npravda.livejournal.com/569855.html	Місцевий розвиток, орієнтований на громаду	02.04.2009	Три громади Тлумацького району стали учасниками проекту Європейського Союзу «Місцевий розвиток, орієнтований на громаду» (СВА) і підписали угоди про співфінансоване партнерство. Проект передбачає заміну старих вікон у школах районів на металопластикові. Про це 3 квітня власкора ЗІКу повідомили у прес-службі Івано-Франківської облдержадміністрації

7	http://odtrk.if.ua/2009/04/02/	Три громади Івано-Франківській області підписали Угоди про партнерство з Проектом ЄС/ПРООН «Місцевий розвиток, орієнтований на громаду»	02.04.2009	Три громади Тлумацького району стали учасниками проекту Європейського Союзу «Місцевий розвиток, орієнтований на громаду» (СВА) і підписали угоди про співфінансоване партнерство. Проект передбачає заміну старих вікон у школах районів на металопластикові. Про це 3 квітня власкора ЗІКу повідомили у прес-службі Івано-Франківської облдержадміністрації
8	http://www.ukurier.gov.ua/index.php?news=1&id=858	Тепло і затишок у школах Прикарпаття 04.04.2009	04.04.2009	Три громади Тлумацького району стали учасниками проекту Європейського Союзу «Місцевий розвиток, орієнтований на громаду» (СВА) і підписали угоди про співфінансоване партнерство. Проект передбачає заміну старих вікон у школах районів на металопластикові. Про це 3 квітня власкора ЗІКу повідомили у прес-службі Івано-Франківської облдержадміністрації
9	http://vsevesti.com/go/ru/article/id/491202/pidpisano-ugodi-pro-partnerstvo.html	Підписано угоди про партнерство	02.04.2009	Три громади Тлумацького району стали учасниками проекту Європейського Союзу «Місцевий розвиток, орієнтований на громаду» (СВА) і підписали угоди про співфінансоване партнерство. Проект передбачає заміну старих вікон у школах районів на металопластикові. Про це 3 квітня власкора ЗІКу повідомили у прес-службі Івано-Франківської облдержадміністрації

KHARKIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Газета "Маяк" Богодухівського району	Ефективне управління організацією громади	04.04.2009	Розповідається про тренінг "Ефективне управління організацією громади", що проведений для 5 ГО Богодухівського району
2	Газета "Главное"	Допомагає нам Європа	11.04.2009	Розповідається про поточний хід реалізації проекту у Первомайському районі.
3	Газета "Знамя труда" Первомайського району	Допомагає нам Європа	11.04.2009	Розповідається про поточний хід реалізації проекту у Первомайському районі.
4	Газета "Дорожня Карта"	Українці власноруч будують «Європу» на селі!	23.04.2009	Розповідається про процес формування громадських організацій у Богодухівському районі. Враження журналіста газети
5	Газета "Знамя труда" Первомайського району	Форум місцевого розвитку району	16.05.2009	Розповідається про поточний хід реалізації проекту у Первомайському районі та ФОРУМИ МІСЦЕВОГО РОЗВИТКУ.
6	Газета "Нове життя" Близнюківського району	"Програма розвитку місцевого самоврядування"	13.06.2009	Розповідається про проведені тренінги для ГО Близнюківського району
Телевізійні репортажі				
1	Обласне телебачення. ТК "ОТБ"	Програма "Новини"	16.04.2009	Розповідається про проведену Обласну координаційну раду проекту, інтерв'ю Др.Саха, В.Гусева.

2	http://www.youtube.com/watch?v=TQHltejbCnQ	Час інформації. Тижневі новини Первомайського району	25.04.2009	Розповідається про тренінг "Ефективне управління організацією громади", що проведений для 5 ГО Первомайського району
3	Телекомпанія "НАДІЯ" Первомайського району	Час інформації. Тижневі новини Первомайського району	16.05.2009	Розповідається про ФОРУМ МІСЦЕВОГО РОЗВИТКУ, що проведений у Первомайському районі.
Радіо репортажі				
1	http://www.esua.info/show/168-l-l-r-1800-1900.html	Радіостанція "Наше радіо"	01.03.2009	Інтерв'ю В.Гусєва - координатора СВА в Харківській області стосовно непоінформованості у проектах ЄС сільських громад
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	http://dk.stop-street.org.ua/?lang=ru&page=publish&show=231	Українці власноруч будують «Європу» на селі!	23.04.2009	Розповідається про процес формування громадських організацій у Богодухівському районі. Враження журналіста газети

КHERSONSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	газета "Новий формат"	"Незабаром у Великоолександрівському районі розпочнуться роботи по впровадженню в життя мікропроектів з освоєння інвестиційних коштів"	17.06.2009 №25 (196)	Про впровадження мікропроектів громад у 5 сільських радах Великоолександрівського району
2	газета "Трудова слава"	"Проект реалізується"	17.06.2009 №47	Про проведення II Форуму місцевого розвитку у Новотроїцькому районі
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	"Херсон.Громада.Ініціатива"	Організація Об'єднаних Націй допоможе сільським громадам Херсонської області" http://www.hgi.org.ua	12.06.2009	Про впровадження проекту в районах області
2	"Бізнес-портал України"	На Херсонщині розпочинається впровадження інвестицій http://ks.ua-katalog.info	15.06.2009	Про впровадження проекту в районах області

КHMELNYTSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Телевізійні репортажі				
1	Районне телебачення	Активні громади	20.05.2009	Виствітлення стану реалізації МП громад в Городоцькому районі
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Бюлетень представництва ЄК в Україні	"Спільний проект ЄС та ООН забезпечив села Хмельниччини шкільним автобусом"	23.04.2009	Про вручення автобуса громаді с.Антоніни та реалізацію проектів в Красилівському районі.

KIROVOHRADSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Вісті Світловодщини	Покращимо життя за рахунок коштів ПРООН	19.03.2009	Впровадження Проекту СВА на території Світловодського району
2	Новоукраїнські новини	Разом дієвіше	14.03.2009	Пріоритетні напрямки та першочергові завдання для громад району
3	Вісті Світловодщини	Місцевий розвиток, орієнтований на громаду	23.04.2009	Перші кроки світловодських громад
4	Новоукраїнські новини	Європейський підхід до розвитку територій	25.04.2009	Проведення тренінгу "Підготовка МПП" для громад Новоукраїнського району
5	Смолінський вісник	Проект Євросоюзу діє у Смоліноу	квітень 2009	Про стан впровадження Проекту СВА на території смт Смолине розповідає заступник селищного голови А.Курбатов
6	Трудова слава	Петрівщина в Проекті TACIS	03.06.2009	Результати засідання ФМР Петрівського району та стан впровадження Проекту СВА на території Петрівщини
7	Маловисківські вісті	Громади захищають своє право на Єврогроші	06.06.2009	Результати першого засідання ФМР Маловисківського району
8	Кіровоградська правда	Розвиток, орієнтований на громаду	05.06.2009	Стан впровадження Проекту на території Олександрівського району
Радіо репортажі				
1	Радіомовлення "Трудова слава" Петрівського району	Пріоритети Проекту СВА актуальні для громад Петрівщини	01.04.2009	Завдання для громад - навчитись чітко формувати потреби і обирати пріоритети

KYIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Вісник Кагарличчини"	"Підписано грантову угоду"	14.04.2009	Про підписання першої грантової угоди в Кагарлицькому районі з громадою с. Мирівка 09.04.2009 р.
2	"Вісник Переяславщини"	"В Єрківцях підписана Угода про фінансування Проекту ООН та ЄС"	28.04.2009	Підписання грантових угод з громадами сіл Єрківці та Жовтнєве Переяслав-Хмельницького району 11.04.2009 р.
3	"Перемога"	Підписані перші грантові угоди за Проектом ЄС/ПРООН	14.05.2009	Про хід впровадження Проекту СВА у Фастівському районі та підписання перших грантових угод з громадами сіл Червона Мотовилівка та Дорогинка 06.05.2009
4	"Миронівський край"	"Громадські ініціативи отримують підтримку"	23.05.2009	Про цілі, завдання та процес впровадження Проекту СВА в Миронівському районі
5	"Вісник Переяславщини"	У Жовтнєвій школі міняють вікна, а у Єрківцях роблять водопровід	23.06.2009	Початок впровадження громадських ініціатив у Переяслав-Хмельницькому районі
Телевізійні репортажі				
1	Телебачення Кагарлицького району ТРС "ТБ Кагарлик"	"Підписано грантову угоду"	11.04.2009	Про підписання першої грантової угоди в Кагарлицькому районі з громадою с. Мирівка 09.04.2009 р.
2	Телебачення Кагарлицького району ТРС "ТБ Кагарлик"	"Підписано грантову угоду"	12.04.2009	Про підписання першої грантової угоди в Кагарлицькому районі з громадою с. Мирівка 09.04.2009 р.

3	Телебачення Миронівка ТБ"	"Урочисте підписання Грантових угод"	24.04.2009	Про підписання першої грантової угоди в Миронівському районі з громадою с. Пії 09.04.2009 р.
4	Телебачення Переяслав-Хмельницького району	"В Єрківцях підписана Угода про фінансування Проекту ООН та ЄС"	24.04.2009	Підписання грантових угод з громадами сіл Єрківці та Жовтнєве Переяслав-Хмельницького району 11.04.2009 р.
5	Телебачення "Миронівка ТБ"	Щодо міжнародної співпраці по впровадженню Проекту	12.05.2009	Щодо міжнародної співпраці по впровадженню Проекту
6	Телебачення Переяслав-Хмельницького району	Підписання грантових угод з громадами сіл Єрківці та Жовтнєве Переяслав-Хмельницького району	25.06.2009	Підписання грантових угод з громадами сіл Єрківці та Жовтнєве Переяслав-Хмельницького району
Радіо репортажі				
1	Районне радіо Кагарлицького району	Реалізація Проекту СВА в Кагарлицькому районі	11.04.2009	Про хід впровадження Проекту СВА в Кагарлицькому районі
2	Районне радіо Кагарлицького району	Реалізація Проекту СВА в Кагарлицькому районі	12.04.2009	Про хід впровадження Проекту СВА в Кагарлицькому районі
3	Районне радіо Кагарлицького району	"Підписано грантову угоду"	14.04.2009	Про підписання першої грантової угоди в Кагарлицькому районі з громадою с. Мирівка 09.04.2009 р.
4	Радіо-студія, Миронівський район	Щодо міжнародної співпраці по впровадженню Проекту	12.05.2009	Щодо міжнародної співпраці по впровадженню Проекту
5	Радіо-студія, Миронівський район	Активність громади с. Пії по енергозберігаючому проекту	10.06.2009	Про впровадження першого в Миронівському районі проекту в школі с. Пії

LUHANSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Життя Білокуракини № 43-44	Обговорення на Форумі	30.05.2009	Обговорення результатів Форуму
2	Кремінщина	Географія проекту СВА в Луганській області	06.06.2009	освітлення діяльності проекту в Луганській області
3	Попаснянський вісник №24	Проект СВА в районі (результати останнього ФМР)	11.06.2009	освітлення результатів Форуму
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	Громадський простір	www.civicua.org/text/news/view.html?q=1211697		

LVIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Наш край - Районний часопис Мостиського району	Візит керівництва ПРООН до Мостиського району.	27.04.2009	Опис візиту – надати допомогу організаціям громад у підготовці та впровадженні проектів громад.
2	«Прикарпатська ватра» - незалежний часопис Старосамбірського району	Громади навчаються готувати проекти до ПРООН	26.04.2009	Опис візиту – надати допомогу організаціям громад у підготовці та впровадженні проектів громад.

3	«Прикарпатська ватра» - незалежний часопис Старосамбірського району	Візит керівництва ПРООН в село Чижки	15.06.2009	Опис зустрічі з громадою села Чижки.
4	Наш край - Районний часопис Мостиського району	В Арламівській Волі відкрили реконструйований медпункт	16.06.2009	Завершення мікропроекту громади. Опис проекту. Опис впровадження Проекту СВА в районі.

MYKOLAIVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Газета "Зоря"	Працюють громади чи не працюють	04.06.2009	про активність громад, які беруть участь у проекті
2	Газета "Южная правда"	800 тис.грн. отримав Снігурівський район	04.04.2009	Про залучення донорського фінансування в Снігурівському районі
Телевізійні репортажі				
1	Март ТК	Новини Миколаївщини	04.06.2009	про проект на миколаївщині - які проблеми обирають громади. про умови участі в проекті
2	35 канал	Прес-клуб	01.04.2009	Про залучення донорського фінансування в Снігурівському районі
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОП/РДА/РР/СВА)				
1	Інформаційна агенція "Контекст Причорномор'я"	Більше 800 тис. грн.грантових коштів залучено в Снігурівський район...	07.04.2009	Більше 800 тис. грн.грантових коштів залучено в Снігурівський район для вирішення важливих соціальних проблем
2	Сайт "Преступності нет"	Снігурівський район отримав 800 тис.грн. грантових коштів	02.04.2009	
3	Сайт "Правда.mk.ua"	Снігурівський район отримав 800 тис.грн. грантових коштів		

ODESKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Телевізійні репортажі				
1	ОДТРК, програма "Роден край"	Сюжет в новинах		СВА в с. Бановка
2	ТК 100%	Інтерв'ю А.Андроновой, контактної особи в ОДА		Стан реалізації проекту
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОП/РДА/РР/СВА)				
1	http://www.prichernomorie.com.ua/odessa/news/international/2009-05-18/62765.php		18.05.2009	
2	http://eho-ua.com/2009/05/18/odesskaja_obladministracija_podpisala_dogovor_s_programmojj_razvitiija_oon_v_ukraine.html		18.05.2009	

3	http://www.novoteka.ru/click/?_URL=http%3A%2F%2Fehua.com%2F2009%2F05%2F18%2Fodesskaja_obladминистрация_подписала_договор_с_программой_развития_ооо_в_ukraine.html		18.05.2009	
4	http://www.nr2.ru/232511.html		18.05.2009	В Одессе 18 мая ожидаются следующие события...

POLTAVSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Решетилівські вісті	Справи громадські	06.04.2009	Про розвиток громад в районі
2	Решетилівські вісті	замітка про форум місцевого розвитку від 22.06.09 (без назви)	24.06.2009	Коротко про зміст засідання форуму та затверджені 2 проекти
3	Народна трибуна	Шкільному автобусу в с. Милорадове бути	16.06.2009	Про відбір проекту ГО "Світанок"
4	Оржицькі вісті	Громадські організації Оржищини взяли участь в Проекті...	16.04.2009	замітка як створити громадську організацію та її можливості
	Пирятинський вісник	Повідомлення про форум місцевого розвитку та затверджені на ньому проекти	07.05.2009	Повідомлення про форум місцевого розвитку та затверджені на ньому проекти
6	Пирятинський вісник	Повідомлення про форум місцевого розвитку та затверджені на ньому проекти	21.05.2009	Повідомлення про форум місцевого розвитку та затверджені на ньому проекти
7	Семенівський край	Європейський шлях розвитку	02.04.2009	Про співпрацю з проектом та обрані пріоритети громад району
8	Козельщинські вісті	Коротка публікація (новина)	09.04.2009	Про форум місцевого розвитку

RIVNENSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Інформ-Полісся	Назустріч покращенню умов життя громад	29.05.2009	Підписання грантової угоди з Томашгородською ГО
2	Дубровицький вісник	Разом дієвіше	29.05.2009	Висвітлення прес-конференції з нагоди впровадження проекту СВА
3	Сарненські новини	Керівники північних районів області дали в Сарнах прес-конференцію	28.05.2009	Про відкриття районного ресурсного центру громад
4	Вісті Рівненщини	Не чакати, а діяти	04.05.2009	Про відкриття районного ресурсного центру громад у Сарненському районі
5	Вісті Кореччини	Місцевий розвиток, орієнтований на громаду	02.04.2009	Про підписання грантових угод з громадами та проектом СВА
Телевізійні репортажі				
1	Місцева телерадіокомпанія "Рівне-1"	інформаційна передача "День"	25.06.2009	Про відкриття районного ресурсного центру громад у Сарненському районі
2	Сфера-TV	Підсумки дня	25.06.2009	Про відкриття районного ресурсного центру громад у Сарненському районі

Радіо репортажі				
1	Рокитнівське районне радіомовлення	новини	26.05.2009	Підписання угоди між ГО та програмою
2	Корецьке районне радіомовлення	Місцеві новини	29.04.2009	радіо-інтерв'ю з координатором обласного ресурсного центру громад щодо прогресу впровадження МП
3	Радивилівське місцеве радіо	новини	26.06.2009	Про засідання Форуму районного розвитку
4	Рокитнівське районне радіомовлення	радіо-інтерв'ю	27.05.2009	коментар контактної особи від Ракитнівської РДА щодо співпраці з проектом СВА
5	Рокитнівське районне радіомовлення	новини	03.06.2009	Про візит польської делегації та їх ознайомлення з роботою громадських організацій району
6	Рокитнівське районне радіомовлення	новини	27.05.2009	інтерв'ю з Філіцом В.
7	Рокитнівське районне радіомовлення	новини	21.04.2009	інтерв'ю з головою РДА щодо співпраці з проектом СВА
8	Рокитнівське районне радіомовлення	новини	14.04.2009	процес впровадження проекту у Рокитнівському районі
9	Заріччянське районне радіомовлення	новини	06.06.2009	процес впровадження проекту у Зарічненському районі
10	Сарненське радіомовлення	інтерв'ю з Філіцом В.	25.06.2009	Про відкриття районного ресурсного центру громад
Публікації у електронних виданнях <i>(не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)</i>				
1	Західно-українська інформаційна корпорація	новини з регіонів	24.05.2009	Про діяльність на Рівненщині проекту СВА, висвітлення показників результативності проекту.

SUMSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Сумщина	Проект ЄС-ПРООН	12.05.2009	Про Впровадження проекту в області
2	В двох словах	Кто рано встает, тому ООН подает...	19.06.2009	Про можливість залучати інвестиції для сільських громад
Телевізійні репортажі				
1	Сумське інтернет-телебачення		25.05.2009	Про стан реалізації проекту в області
Радіо репортажі				
1	Буринське районне радіо		19.06.2009	Про стан реалізації проекту в районі
2	Середино-Будське районне радіо		11.06.2009	Про стан реалізації проекту в районі

TERNOPILSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Нова ера	У Тернополі рекламували європейські країни	27 травня- 2 червня 2009	Розповідь про відкриття мікропроекту "Шкільний автобус" у с.Вишгородок та продовження святкування днів Європи у м.Тернополі

2	Місто	Деяким селам області "підкинуть" грошей	27.05.2009	Розповідається про зустріч керівництва області із Представником ПРООН Ерджаном Муратом , а також про виділення 1 млн. грн. Тернопільською обласною радою для 40 громад, які беруть участь у Проекті
3	Нова Тернопільська газета	"Шкільний автобус" від послів	27.05.2009	Розповідається про реалізацію мікропроєкт "Придбання шкільного автобуса" у с.Вишгородок
4	Голос Лановеччини	Вінець співпраці - Шкільний автобус	29.05.2009	Розповідається про реалізацію мікропроєкт "Придбання шкільного автобуса" у с.Вишгородок Лановецького району
5	Вісник Надзбруччя	Новини райдержадміністрація	19.06.2009	Інформація про проведення засідання ФМР
Телевізійні репортажі				
1	ТТБ (Телебачення)	Вісті ТТБ	25 травня 2009 (20:00 та 22:00 год.)	Розповідається про реалізацію мікропроєкт "Придбання шкільного автобуса" у с.Вишгородок Лановецького району
Радіо репортажі				
1	Обласне радіо	Новини	25 травня 2009 (18:10 год.)	Розповідається про реалізацію мікропроєкт "Придбання шкільного автобуса" у с.Вишгородок Лановецького району
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОР/РДА/РР/СВА)				
1	20 хвилин	Головний майдан Тернополя перетворився на Європейське містечко http://te.20minut.ua/news/150051	23.05.2009	Святкування днів Європи у м.Тернополі та відкриття шкільного автобуса в с.Вишгородок Лановецького району
2	News.te.ua	Громада Вишгородка, що на Лановеччині, отримала «шкільний автобус» http://ua.redtram.com/go/201921539/	23.05.2009	Відкриття шкільного автобуса в с.Вишгородок Лановецького району
3	Українське національне інформаційне агенство	День Європи голова Представництва Єврокомісії в Україні та іноземні посли провели в Тернополі http://www.ukrinform.ua/ukr/order/?id=809842	23.05.2009	Святкування днів Європи у м.Тернополі та відкриття шкільного автобуса в с.Вишгородок Лановецького району
4	Нова Ера	Жозе Мануель Пінту Тейшейра: «Україні потрібні реформи і політична стабільність» http://novaera.te.ua/article_view.php?article=2616	23.05.2009	Святкування днів Європи у м.Тернополі та відкриття шкільного автобуса в с.Вишгородок Лановецького району
5	Незалежне інформаційно-аналітичне інтернет видання zaxid.net	Тернопільська облрада виділила 1 млн грн на фінансування 40 мікрогромад http://www.zaxid.net/newsua/2009/5/25/194721/	25.05.2009	Розповідається про виділення Тернопільською обласною радою коштів 40 громадам на співфінансування Проєкт "Місцевий розвиток, орієнтований на громаду"
6	Zik	Тернопільська громада реалізувала власний мікропроєкт «шкільний автобус» http://zik.com.ua/ua/news/2009/05/25/182001	25.05.2009	Відкриття шкільного автобуса в с.Вишгородок Лановецького району

7	Smile - tv	У рамках проведення днів Європи Тернопіль відвідали 8 послів країн-членів ЄС http://smiletv.te.ua/del/index.php?option=com_content&task=view&id=1022&Itemid=1	25.05.2009	Святкування днів Європи у м.Тернополі та відкриття шкільного автобуса в с.Вишгородок Лановецького району
8	Голос України	ЄС допоміг школярам отримати автобус, а туристам - велосипед http://www.golos.com.ua/article.aspx?id=134926	26.05.2009	Святкування днів Європи у м.Тернополі та відкриття шкільного автобуса в с.Вишгородок Лановецького району
9	УХрадіо – українське інтернет радіо	Громада вишгородка, що на Лановеччині, отримала «шкільний автобус» http://www.uhradio.com.ua/article/2009/may/26/gromada-vishgorodka-sho-na-lanovechchini-otrimala/	26.05.2009	Відкриття шкільного автобуса в с.Вишгородок Лановецького району

VINNYTSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друківані публікації				
1	Газета "Вінниччина"	"Шкільний автобус" на Бершадщині	19.06.2009	Інформація про Завершення проекту "Шкільний автобус"
2	Газета "Бершадський край"	Г.М. Заболотний: нас єднає Бершадська земля	24.06.2009	Участь голови Вінницької обласної ради у відкритті Шкільного автобуса
Телевізійні репортажі				
1	Вінницька обласна державна телерадіокомпанія	"Шкільний автобус" на Бершадщині	19.06.2009	Інформація про Завершення проекту "Шкільний автобус"
Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОП/РДА/РР/СВА)				
1	http://www.bershad.ua	Г.М. Заболотний: нас єднає Бершадська земля	24.06.2009	Участь голови Вінницької обласної ради у відкритті Шкільного автобуса

VOLYNska OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друківані публікації				
1	"Волинь"	Сільські громади підтримує... ООН	28.05.2009	Опис робочої наради проекту та огляд діяльності за перший рік роботи.
Телевізійні репортажі				
1	ТРК "Волинь-Нова"	Новини	25.05 та 26.05.2009	ЄС та ООН допомагають волинським селам. Станом на 1.05.09р. Подано на співфінансування 25 проектів громад, на 12 з яких з обласного бюджету виділено перший транш - 500.тис.грн.

Публікації у електронних виданнях (не рахуючи повідомлень на веб сайтах ОДА/ОП/РДА/РР/СВА)				
1	Волинська правда	ООН буде більше фінансувати Волинь через програми розвитку	25.05.2009	Під час зустрічі з головою Волинської облдержадміністрації Миколою Романюком Уповноважений керівник офісу ПРООН в Україні Ерджан Мурат заявив, що під час найближчої зустрічі з фінансовими донорами Проекту «Місцевий розвиток, орієнтований на громаду» порушить питання щодо збільшення фінансування Волині»
2	Волинська правда	Найбільше проектів місцевих громад Волині стосуються енергозбереження	25.05.2009	Наразі на Волині реалізуються 40 проектів розвитку територіальних громад із залученням коштів Програми розвитку ООН в Україні та та ЄС, та співфінансування з боку місцевих громад. Про це йшлося на робочій нараді проекту «Місцевий розвиток, орієнтований на громаду», який відбувся 25 травня.
3	Волинська правда	В одному з сіл Ратнівщини постане ресурсний центр	25.05.2009	Станом на 1 травня на реалізацію на 12 мікропроектів в рамках програми «Місцевий розвиток, орієнтований на громаду» вже засвоєно 2 мільйони 191 тисячу 619 гривень. Цю цифру, під час робочої наради, назвав заступник голови ОДА Василь Байцим.
4	Волинські новини	Волинська влада на закордонні гроші робить "євроремонт в головах людей"	25.05.2009	Голова Волинської обласної ради Анатолій Грицюк розповів, що однією із цілей цього проекту є не лише поліпшення інфраструктури сіл та селищ Волині, а й навчання місцевих громад «не ждати манни небесної у вигляді субвенції, а намагатися вирішити власні проблеми самотужки».
5	Волинські новини	Іноземці не розуміють навіщо українським селам "концертні зали" та "сауни"	25.05.2009	Своєрідний майстер-клас із написання проектів волинським посадовцям дав старший менеджер ПРООН в Україні Сергій Волков. Про це йшлося сьогодні, 25 травня, під час робочої наради Проекту «Місцевий розвиток, орієнтований на громаду» в області

ZAKARPATSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	Газета "Вісник Берегівщини"	"На Форумі місцевого розвитку"	25.04.2009	Про затвердження мікропроектів ПРООН та ЄС та підтримку громад з боку районної ради.
2	Газета "Голос Верховини"	"Партнерство вимагає організованості"	16.05.2009	Про підготовку мікропроектів ПРООН та ЄС та фінансову підтримку громад з боку районної ради.
3	Газета "Вісті Свалявщини"	"Чи готові громади до реалізації власних ініціатив"	30.05.2009	Про вибір пріоритетних проблем громадами району та головність мікропроектів ПРООН та ЄС .

ZAPORIZKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	"Наше життя"	"Усією громадою подбаємо про своє селище"	№41- 04.06.09	Про звіт голови щодо плану розвитку ГО
2	"Запорізька Правда"	"Гранди від ПРООН отримали ще дві громади"	№83 -13.06.09	Про підписання угоди між ГО "КЗОГ", "Прогрес" та ПРООН
3	"Запорізька Правда"	"Грантова Угода"	№73 -26.05.09	Про підписання угоди між ГО "Відродження" та ПРООН
4	"Голос Гуляйпілья"	"Угода перша, але не остання"	№ 43 -06.06.09	В районі підписана перша угода з ПРООН....
5	"Ринг-експрес"	"Гюновка веселит- Бановка немного огорчает"	№ 48 -18.06.09	Про приїзд координатора у Запорізькій області до району та перевірка МПП громад
6	"Рідний край"	"Ще дві громади можуть отримати грант ПРООН"	№47 -17.06.09	Про підписання угоди між ГО "КЗОГ", "Прогрес" та ПРООН
7	"Запорізька Правда"	"Діяти самостійно на користь громаді"	№84 -16.06.09	Про координаційну раду
8	"Ринг-експрес"	"Коларовка имеет шанс получить грантовую помощь"	№49 - 23.06.09	Про проведення ФМР та затвердження МПП с.Коларівка
9	"Приморская степь"	" В районе прошел Форум местного развития"	№44 - 27.06.09	Про проведення ФМР та затвердження МПП с.Коларівка
Телевізійні репортажі				
1	ТВ - 5	Про проведення координаційної ради у м.Запоріжжя	12.06.2009	Про проведення координаційної ради у м.Запоріжжя та обговорення сум фінансування
2	5 канал	Про розвиток українських громад	21.06.2009	Досвід, отриманий ГО с.Підгірне Новомиколаїського р-ну під час реалізації Проекту ПРООН

ZHUTOMYRSKA OBLAST

№	Назва видання	Назва публікації та посилання (для електронних ЗМІ)	Дата	Короткий зміст
Друковані публікації				
1	газета "Нове життя"	"Дружній візит на високівську землю"	17.04.2009	про візит керівництва Проекту У громаду села Високого
2	"Коростишівська газета"	"Студениця: угоду підписано. Розпочинаються роботи"	30.04.2009	про 3 діалог
3	"Новини Андрушівщини"	"Громада орієнтується на розвиток"	17.04.2009	про засідання ФМР
Телевізійні репортажі				
1	"Союз ТВ"	Новини	29.04.2009	Про ОКР
2	"Союз ТВ"	Новини	29.04.2009	Про ОКР
3	"Союз ТВ"	Новини	29.04.2009	Про ОКР
4	"Союз ТВ"	Новини	30.04.2009	Про ОКР
5	"Союз ТВ"	Новини	30.04.2009	Про ОКР
6	Обласне телебачення	Новини	29.04.2009	Про ОКР
7	Обласне телебачення	Новини	29.04.2009	Про ОКР
8	Обласне телебачення	Новини	29.04.2009	Про ОКР
9	Обласне телебачення	Новини	30.04.2009	Про ОКР
10	Обласне телебачення	Новини	30.04.2009	Про ОКР
Радіо репортажі				
1	Обласне радіо	Новини	29.04.2009	Про засідання ОКР
2	Обласне радіо	Новини	29.04.2009	Про засідання ОКР
3	Обласне радіо	Новини	29.04.2009	Про засідання ОКР

Annex - XIX
Summary of News Publications on Partner's Web-sites

CHERKASKA OBLAST

#	Date	Site	Title of publication
1	25.06.2009	http://www.oblrada.ck.ua/news/2494098.html	Підбито перші підсумки реалізації проекту ПРООН «Місцевий розвиток, орієнтований на громаду»

CHERNIHIVSKA OBLAST

#	Date	Site	Title of publication
1	16.04.2009, 14.05.2009, 26.06.2008	Сайт ОДА	Про реалізацію Проекту "Місцевий розвиток, орієнтований на громаду" (1 . Підсумки за 2008 рік., 2 Підписано 4 угоди з ОГ, 3. Перший транш)

DNIPROPETROVSKA OBLAST

#	Date	Site	Title of publication
1	11.06.2009	офіційний сайт обласної ради http://oblrada.dp.ua	Підписано угоду про партнерство між Програмою розвитку Організації Об'єднаних Націй та Дніпропетровською обласною радою

IVANO-FRANKIVSKA OBLAST

#	Date	Site	Title of publication
1	26.05.2009	http://gorrayrada.if.ua/news/latest/1-news/136-2009-06-02-08-54-34	II-й Форум місцевого розвитку
2	28.04.2009	http://gorrayrada.if.ua/news/latest/1-news/132-2009-05-07-10-44-51	Засідання круглого столу
3	02.04.2009	http://www.gov.if.ua/modules.php?name=News&file=article&sid=9421	Підписано угоди про партнерство

KHARKIVSKA OBLAST

#	Date	Site	Title of publication
1	16.04.2009	http://www.kharkivoda.gov.ua/news.php?news=9772	Олександр Колесніков провів перше засідання обласної координаційної ради проекту ЄС "Місцевий розвиток, орієнтований на громаду"
2	17.04.2009	http://www.oblrada.kharkov.ua/rus/news/?id=2827	ПРОГРАММА «МЕСТНОЕ РАЗВИТИЕ, ОРИЕНТИРОВАННОЕ НА ГРОМАДУ» ЗАСТАВЛЯЕТ ТЕРРИТОРИАЛЬНЫЕ ГРОМАДЫ САМОСТОЯТЕЛЬНО РЕШАТЬ СВОИ ПРОБЛЕМЫ
3	17.04.2009	http://www.oblrada.kharkov.ua/rus/news/?id=2822	Сельские советы готовятся к участию в проекте ООН
4	24.04.2009	http://www.kharkivoda.gov.ua/show.php?page=19923	Громадські організації утворені. Вже сім районів Харківської області ознайомлені з Ефективним управлінням і плануванням діяльності організацій громад. Проект Євросоюзу та ПРООН.
5	14.05.2009	http://www.kharkivoda.gov.ua/news.php?news=9903	Розповідається про участь координатора проекту СВА Гусева у заході "Європейська п'ятниця відкритих дискусій"
6	12.06.2009	http://www.kharkivoda.gov.ua/show.php?page=20641	Форуми місцевого розвитку на Харківщині - затверджено перші мікропроекти громад

KHERSONSKA OBLAST

#	Date	Site	Title of publication
1	05.04.2009	oda.kherson.ua	"Інформаційно-аналітичний звіт про реалізацію проекту ЄС/ПРООН "Місцевий розвиток, орієнтований на громаду" за 2008 рік"
2	14.04.2009	oblrada.ks.ua	"Обласна рада представляє та захищає інтереси територіальної громади Херсонщини"
3	16.04.2009	oda.kherson.ua	"На Херсонщині триває реалізація проекту Європейської Комісії та Програми розвитку ООН в Україні "Місцевий розвиток, орієнтований на громаду"
4	17.04.2009	oda.kherson.ua	"Форуми місцевого розвитку спрямовують свою роботу на допомогу активним громадам"
5	12.06.2009	oda.kherson.ua	"Незабаром у Великоолександрівському районі розпочнуться роботи по впровадженню в життя мікропроектів з освоєння інвестиційних коштів"

KHMELNYTSKA OBLAST

#	Date	Site	Title of publication
1	16.04.2009	www.adm.km.ua	"Новий автобус для дітлахів"
2	16.04.2009	www.oblrada.km.ua	В рубриці "Робочі будні обласної ради"
3	15.04.2009	www.cba.org.ua	"Шкільний автобус - перший завершений проект антонінської громади"
4	05.05.2009	www.slavuta-rda.com	"Славутчина навчається"

KIROVOHRADSKA OBLAST

#	Date	Site	Title of publication
1	27.03.2009	Офіційний сайт Кіровоградської обласної державної адміністрації	Інформація про потенційні проекти в рамках ініціативи «Кожна Краплина Має Значення»
2	07.04.2009	Офіційний сайт Кіровоградської обласної ради	Інформаційний бюлетень
3	10.04.2009	Офіційний сайт Кіровоградської обласної державної адміністрації	Перемога в проекті «Кожна краплина має значення» - нове життя для Новомиргородського джерела
4	28.04.2009	Офіційний сайт Кіровоградської обласної ради	Перші грантові угоди на Кіровоградщині
5	18.04.2009	Офіційний сайт Кіровоградської обласної державної адміністрації	Новини про стан впровадження в Кіровоградській області Проекту «Місцевий розвиток, орієнтований на громаду»
6	22.05.2009	Офіційний сайт Кіровоградської обласної ради	Інформаційний бюлетень
7	03.06.2009	Офіційний сайт Кіровоградської обласної ради	Інформація про стан впровадження в Кіровоградській області Проекту «Місцевий розвиток, орієнтований на громаду»
8	16.06.2009	Офіційний сайт Кіровоградської обласної ради	Доля співфінансування проектів громад вирішується на форумах
9	29.06.2009	Офіційний сайт Кіровоградської обласної ради	Відбувся тренінг для скарбників громадських організацій – учасників Проекту СВА

LUHANSKA OBLAST

#	Date	Site	Title of publication
1	15.04.2009	http://stb.loga.gov.ua/activity/economy/investments/	Звіт про оглядовий візит за результатами роботи Проекту СВА в Луганській області
2	15.04.2009	bv.loga.gov.ua/activity/economy/investments/	про візит до Луганську керівників проекту
3	02.06.2009	http://pps.loga.gov.ua/activity/press/news-pps/2009/06/02/news-pps_8262.html	Відбулось засідання Форуму місцевого розвитку Проекту ПРООН
4	10.06.2009	http://stb.loga.gov.ua/activity/economy/investments/	про результати проведення ФМР
5	11.06.2009	bv.loga.gov.ua/activity/economy/investments/	про результати проведення ФМР
6	17.06.2009	http://svt.loga.gov.ua/activity/press/news-svt/	про робочу поїздку координатора до громади

LVIVSKA OBLAST

#	Date	Site	Title of publication
1	29.04.2009	http://mostyska-rda.gov.ua/press-center	Нові громади вступають в проект. Раденичі та Буховичі. На сході сіл створено ініціативні групи, які будуть займатися реконструкцією ФАПів.
2	15.06.2009	http://www.list.lviv.net/	Свято для громади. В Арламівській Волі Мостиського району відбулося урочисте відкриття ФАПу
3	15.05.2009	http://golos.prykarpaty.net	В ОНОВЛЕНОМУ КОРНАЛОВИЦЬКОМУ НАРОДНОМУ ДОМІ ПЕРШИМ БУЛО СВЯТО. Планування ремонту ФАПу, на що потрібно близько 200 тисяч гривень.
4	11.06.2009	www.loda.gov.ua	Місцевий розвиток, орієнтований на громаду Сприяння сталому соціально-економічному розвитку на місцевому рівні через підтримку та співфінансування громадських ініціатив

MYKOLAIVSKA OBLAST

#	Date	Site	Title of publication
1	20.04.2009	ОДА	про підготовку МПП в районах
2	22.05.2009	ОДА	про проведення семінару в Вознесенську
3	02.06.2009	ОДА	про проект (присвячено дню європи)

ODESKA OBLAST

#	Date	Site	Title of publication
1	23.05.2009	http://ved.odessa.gov.ua/Main.aspx?sect=Page&IDPage=19318&id=1150	
2	18.05.2009	ОДА	анонс зустрічі голови ОДА з менеджментом проекту
3	22.05.2009	Болградська РДА	повідомлення про підписання контракту
4	01.06.2009	СВА	Підписання угоди про співпрацю

RIVNENSKA OBLAST

#	Date	Site	Title of publication
1	13.06.2009	Офіційний сайт Рівненської ОДА	Проведення тренінгу для бухгалтерів ГО
2	16.05.2009	Офіційний сайт Сарненської РДА	Проведення тренінгу по впровадженню МП для громад
3	23.05.2009	Офіційний сайт Рокитнівської РДА	Підписання грантової угоди з Томашгородською ГО "Прометей"
4	26.05.2009	Офіційний сайт Сарненської РДА	Про відкриття районного ресурсного центру громад
5	28.05.2009	Офіційний сайт Корецької РДА	Про успіх громад у реалізації проектів і надходження перших трансів

SUMSKA OBLAST

#	Date	Site	Title of publication
1	05.05.2009	http://www.oblrada.sumy.ua/index.php?option=com_content&task=view&id=3254&Itemid=1	Перші в Тростянецькому районі – перші в області
2	22.05.2009	http://www.oblrada.sumy.ua/index.php?option=com_content&task=view&id=3303&Itemid=1	Угоду уклали? Чекайте на фінансування проекту
3	30.04.2009	http://www.state-gov.sumy.ua/docs/euro.htm	Підписання першої угоди про співпрацю в рамках реалізації Проекту ЄС/ПРООН «Місцевий розвиток, орієнтований на громаду»
4	26.05.2009	http://state-gov.sumy.ua/2009/05/26/koshti_pracjujut_na_gromadu.html	КОШТИ ПРАЦЮЮТЬ НА ГРОМАДУ
5	30.04.2009	http://cba.org.ua	Підписання першої угоди про співпрацю в рамках реалізації Проекту ЄС/ПРООН «Місцевий розвиток, орієнтований на громаду»
6	29.04.2009	http://cba.org.ua	Перший проект Сумської області отримає фінансування від Проекту "Місцевий розвиток, орієнтований на громаду"
7	25.05.2009	http://www.oblrada.sumy.ua/index.php?option=com_content&task=view&id=3309&Itemid=108	Підписано грантову угоду на фінансування ініціативи громади
8	08.04.2009	http://cba.org.ua	Визначено переможців Всеукраїнського конкурсу "Кожна краплина має значення"

TERNOPILSKA OBLAST

#	Date	Site	Title of publication
1	13.05.2009	Лановецька РДА, http://lanivtsi.net/index.php?rozd=2&id=347	Виїзний день прийому громадян головою рдаи у Бережанській сільській раді, зустріч з членами сільського комітету с.Вишгородок.
2	23.05.2009	Тернопільська ОДА, http://www.oda.te.gov.ua/index.php?action=show&id=8607	Громада Вишгородка, що на Лановеччині, отримала «шкільний автобус»
3	24.05.2009	ПРООН, http://undp.org.ua/ua/media/44-local-development-and-human-security/800-local-communities-launch-school-bus-initiative-allowing-children-from-eight-villages-attend-school-on-time	В Тернопільській області урочисто відкрито маршрут шкільного автобусу для дітей з восьми сіл
4	24.05.2009	СВА, http://www.cba.org.ua/generalnews/news_tn_230509.aspx	В Тернопільській області урочисто відкрито маршрут шкільного автобусу для дітей з 8 сіл

5	25.05.2009	Тернопільська ОДА, http://www.oda.te.gov.ua/index.php?action=snow&id=8613	"Тернопільська область готова до продовження участі у проєкті ПРООН"
6	25.05.2009	Тернопільська обласна рада, http://www.obl-rada.te.ua/?page=news&newsid=1289	Один мільйон гривень виділено із обласного бюджету на співфінансування мікропроєктів 40 місцевих громад.

VINNYTSKA OBLAST

#	Date	Site	Title of publication
1	19.06.2009	www.vin.gov.ua	робочий візит

ZAKARPATSKA OBLAST

#	Date	Site	Title of publication
1	25.04.2009	bereg-rda.gov.ua	На Форумі місцевого розвитку
2	12.06.2009	zak-rada.gov.ua	На порядку денному - розвиток місцевих громад

ZAPORIZKA OBLAST

#	Date	Site	Title of publication
1	01.04.2009	www.zoda.gov.ua	Ініціативи громад втілились у їхніх власних проєктах
2	15.06.2009	www.zoda.gov.ua	Сільські громади регіону доводять свою дієвість
3	15.06.2009	www.rada.zp.ua	Обласна Рада підтримує розвиток громад
4	15.06.2009	www.rada.zp.ua	Проєкт «Місцевий розвиток, орієнтований на громаду»

Annex – XX
Publication and Dissemination of Regional Newsletters

#	Oblast	Newsletters since inception		
		No of issues published	No of copies printed & distributed	No of copies sent electronically
1	ARC	4	250	75
2	Cherkaska	4	250	200
3	Chernihivska	6	300	300
4	Chernivetska	3	300	240
5	Dnipropetrovska	1	100	0
6	Donetska	1	50	75
7	Ivano-Frankivska	10	1120	172
8	Kharkivska	6	2487	355
9	Khersonska	3	300	180
10	Khmelnyska	2	200	200
11	Kirovohradska	3	200	200
12	Kyivska	5	830	830
13	Luhanska	6	1520	292
14	Lvivska	3	300	26
15	Mykolaivska	4	900	280
16	Odeska	10	1850	10
17	Poltavska	5	640	0
18	Rivnenska	3	107	116
19	Sumska	6	3870	530
20	Ternopil'ska	5	430	100
21	Vinnytska	4	1000	700
22	Volynska	2	300	100
23	Zakarpatska	5	1150	1150
24	Zaporizka	8	3695	1935
25	Zhytomyrska	3	750	50
Total		112	22899	8116
